

# **eCourts Mission Mode Project**

## **Monthly Project Progress Summary**

**1 Aug 2013 – 31 Aug 2013**


## Table of Contents

1. Country-wide progress status summary ..... 3
2. Monthly Progress Report of e-Courts Mission Mode Project for Aug 2013 ..... 4

# 1. Country-wide progress status summary

The following table shows the status (in courts) of project implementation across the country, as of 31 Aug, 2013; excluding Delhi.

**Country wide status – District and Subordinate Courts**

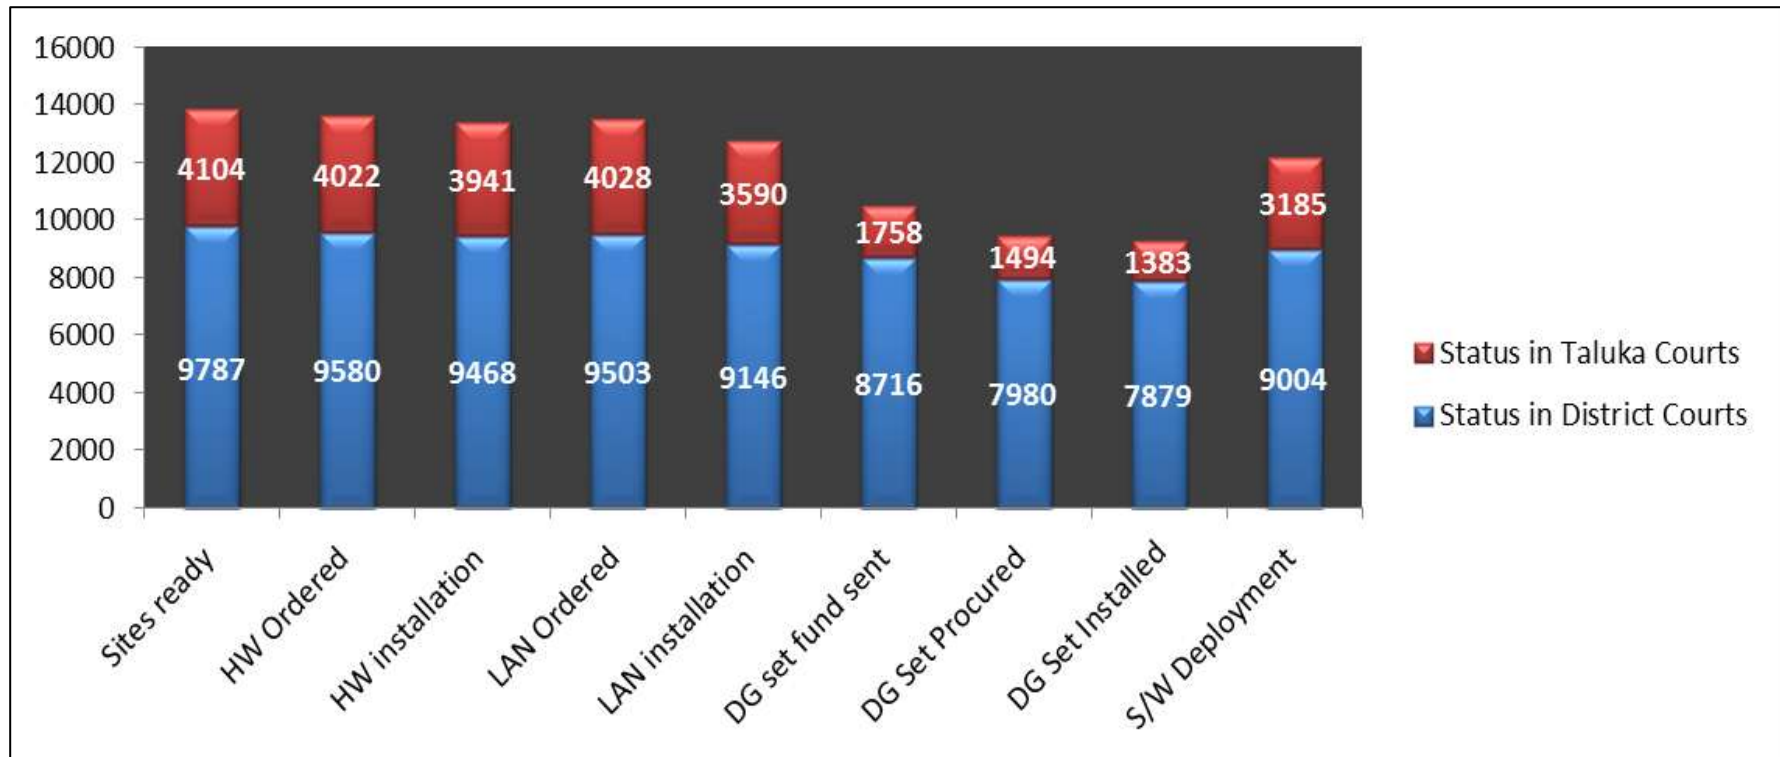

## **2. Monthly Progress Report of e-Courts Mission Mode Project for Aug 2013**

- 1. Site Preparation completed at 12 Court Complexes (CCs) (45 Courts):** Chhattisgarh – 6 CCs, Gauhati – 5 CCs, and Karnataka – 1 CC
  
- 2. Computer hardware for district & subordinate courts:**
  - ▶ **Hardware ordered at 30 Court Complexes (CCs) (120 Courts):** Allahabad – 3 CCs, Andhra Pradesh – 5 CCs, Chhattisgarh – 7 CCs, Gujarat – 4 CCs, Madras – 7 CCs, and Uttarakhand – 4 CCs
  - ▶ **Hardware installation completed at 1 Court Complexes (CCs) (1 Court):** Allahabad – 1 CC
  
- 3. LAN installation at district & subordinate courts:**
  - ▶ **LAN ordered at 14 Court Complexes (20 Courts):** Allahabad – 5 CCs, Andhra Pradesh – 3 CCs, Chhattisgarh – 4 CCs, Gujarat – 1 CC, and Rajasthan – 1 CC
  - ▶ **LAN delivered at 12 Court Complexes (CCs) (65 Courts):** Allahabad – 8 CCs, Maharashtra – 1 CC, Gujarat – 1 CC, Gauhati – 1 CC, and Jharkhand – 1 CC
  - ▶ **LAN installation completed at 24 Court Complexes (CCs) (177 Courts):** Allahabad – 3 CCs, Andhra Pradesh – 1 CC, Maharashtra – 4 CCs, Jharkhand – 1 CC, Madras – 1 CC, Orissa – 7 CCs, Bihar – 7 CCs
