

eCourts Mission Mode Project

Monthly Project Progress Summary and Key Issues

1 December 2010 - 31 December 2010


Table of Contents

- 1. Country-wide progress status summary 3
- 2. High Court wise issues..... 5


1. Country-wide progress status summary

The following two figures show the status of project implementation across the country, as of December 31, 2010. It also shows the increment in the various modules in December.

For the purpose of clarity, the status has been reported in terms of Courts as well as in Court Complexes in figure I and figure II respectively.

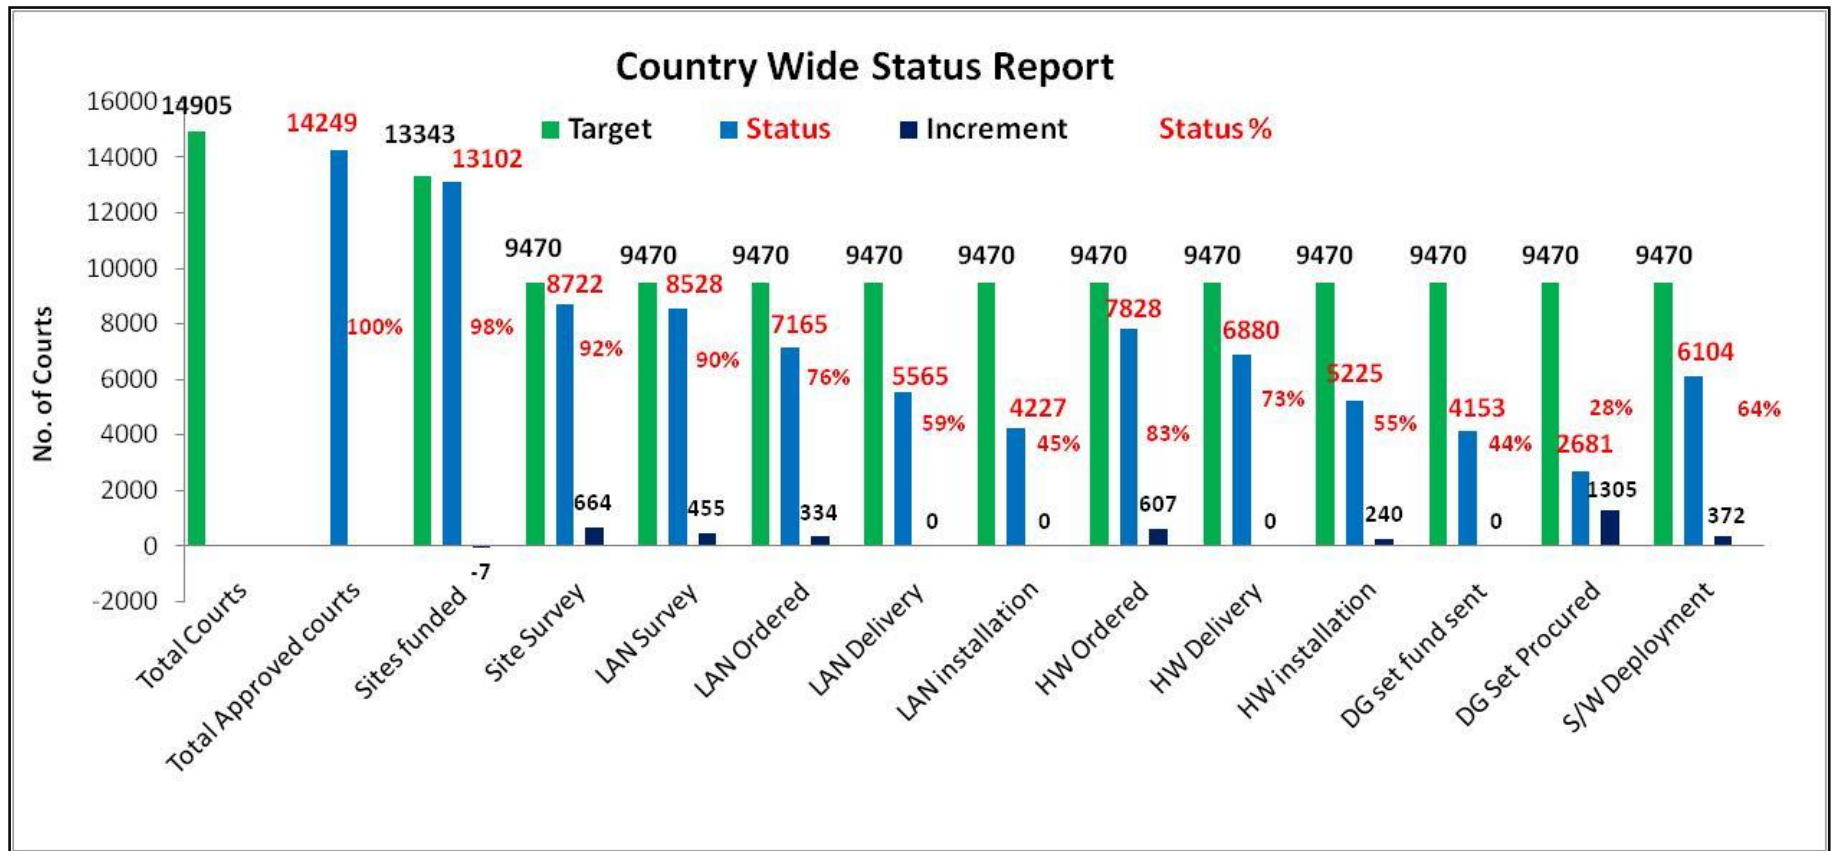

For the Time Period: 1 - 31 December 2010
 Figure I: Country Wide Status Reports (Courts)

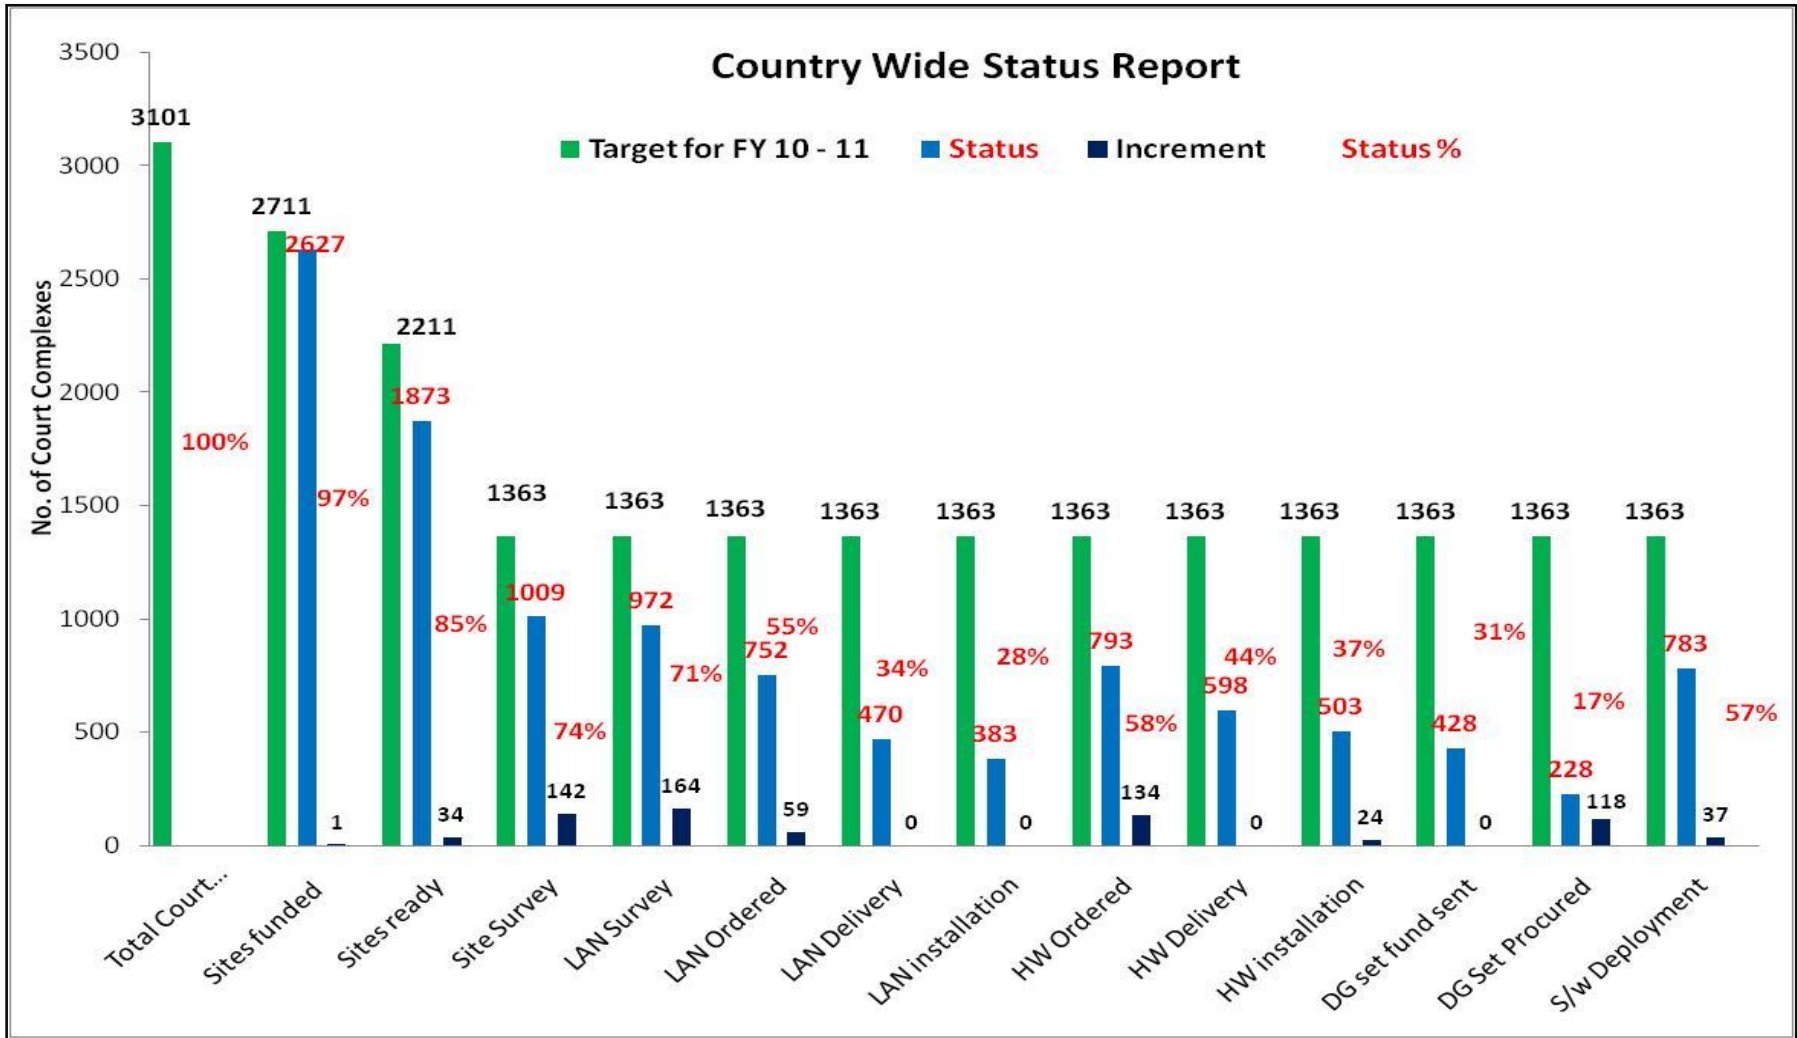

For the Time Period: 1 - 31 December 2010

Figure II: Country Wide Status Reports (Court Complexes)

2. High Court wise issues

The following list highlights issues in project implementation that need to be addressed by the stakeholders listed.

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
Allahabad	Sites where installation is halted due to site non readiness to be made ready and handed over to vendor for HW / LAN installation.	To expedite hardware / LAN installation at District CCs (court complexes) - Schedule to be given to NIC / HC.	Stringent monitoring of vendor progress to be done to achieve target completion.
	Cost Estimates for DG Sets to be sent for 70 DCs where HW ordered		
AP	Site Preparation activity to be expedited by HC for 237 CCs.	Vendor M/s HCL to take up the LAN Survey at 2 CCs	Fund transfer for DG set procurement at 56 taluka court complexes to be taken up.
	DG set procurement to be expedited by the HC at 9 CCs.	Vendor M/s HCL to initiate delivery and installation of Hardware material at 8 District CCs for which order issued in Nov'10.	Funds to be transferred for DG sets for pending 11 CCs
	Selection of technical manpower to be taken up by HC		LAN and Hardware Installation orders for 14 CCs to be issued.
	Deployment of Application software to be taken up for balance 22 CCs.		
	Site readiness for HC LAN installation to be given by HC.		
Bombay	DG sets to be procured at 22/120 CCs.	LAN installation to be completed at pending 22 CCs.	
	Initiation of site preparation work at 256 CCs.	LAN survey to be completed at 34 CCs where HW PO issued.	

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
Calcutta	DG set procurement to be taken up at pending 12 out of 22 district court complexes, for which funds were sent by NIC in March 2010.	Hardware installation to be expedited at 41 taluka court complexes, for which orders were issued in Jan / Feb 2010	Fund transfer for DG set procurement at 56 taluka court complexes to be taken up.
	Site Preparation of the Andaman Bench to be expedited. Hardware and LAN installation material delivered since almost an year, however not installed due to site non readiness.	LAN material delivery and installation to be started at 63 taluka court complexes (orders issued in Sep / Nov 2010), so that work is completed by March 2011.	CIS software training to be provided at the Andaman District Court
	Old / New LAN integration, data migration and court staff training on eCourts application software to be taken up at the remaining 2 / 22 District Court complexes.		
	Issue of missing LAN material at High Court to be resolved.		
	Site to be prepared for the installation of UPS delivered at High Court and district court of South 24 Parganas since past six months.		
	Feedback wrt CIS software to be provided to NIC HQ as per the feedback obtained from district court complexes during trial run		
Chhattisgarh	Site Preparation cost estimates to be sent for 28 Taluka CC	N/A	Funds for DG set for 14 CCs initiated.
			Funds for site preparation at 25 CCs initiated.
			Above to be sent to HC.

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
Gujarat	Gaps pending in 29/41 Sites to be rectified. Revised SRVFs to be submitted.	To expedite LAN survey at 120 ready CCs.	N/A
	Site preparation to be completed at the balance CCs	LAN survey report for 36 CCs to submitted to NIC HQ for LAN PO Issuance.	
	DG Set to be procured at 54 CCs.		
Guwahati	Pending site preparation to be completed at 12 CCs where funds already sent.	LAN installation to be completed at 29 CCs- PO issued in July'10	HW POs to be issued for 3 CCs where LAN PO issued recently.
		LAN survey to be completed at balance 24 ready CCs.	
Jammu & Kashmir	CPC to analyse the feasibility of LAN / HW Installation in the Taluka Courts of Kashmir region through some local agency.	Taluka Site/LAN Survey to be started by HCL in the Jammu Region at 14 sites.	SW installation to be expedited.
	CPC to propose an action plan for LAN / HW Material delivery and Installation in the District Courts situated in Leh and Kargil, since the accessibility for these regions is cut off for the most part of the year.	HW/ LAN Installation to be expedited at the remaining District Courts by WIPRO.	
Jharkhand	Cost estimates for site preparation to be sent within the approved limit of 2.75 lacs for the ten taluka court complexes pending for site preparation funding.	Vendor to complete hardware and LAN installation at the 27 court complexes for which orders have been issued in July / August 2010.	
	Cost estimates for DG sets to be sent by the HC to NIC for the 27 court complexes, for which hardware / LAN orders have been issued, for requisite fund	Finalised LAN survey reports to be submitted at NIC HQ for further PO release.	

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
	transfer.		
Karnataka	Site Readiness reported at 119 CCs, 6/119 CCs found as NOT ready. Gaps to be rectified.	To expedite LAN survey at ready taluka CCs (83).	HW / LAN POs to be issued for DCs where survey completed.
	DG Set to be procured at 7 CCs.	HW / LAN installation to be completed at DCs.	
Kerala	Selection for pending technical manpower to be taken up.	LAN survey to be completed at 77 Taluka CCs	N/A
	DG Sets to be procured at all 40 district court complexes.		
Madras	Pending site preparation to be completed at taluka level.	LAN Survey and submission of BOM documents to be completed for 27 court complexes - HP.	L3 switches delivery pending for 4 district Court complexes.
	DG Set to be procured at balance 43 district courts complexes.	LAN installation pending for two courts- Wipro.	
	DG set estimates for taluka court complexes to be forwarded to NIC HQ.		
MP	Pending site preparation cost estimates to be sent to NIC (13).	DG sets to be installed at 39 Districts. The process has been delayed because PWD has got approval for cable length of 10 m only while as they require more than that.	DG set funds to be sent for 4 DCs.
	DG sets to be procured at 39 DCs but need to install at those sites.		Approval from e-committee for recruitment of System Assistants (76).
	Technical manpower need to be deployed. (7 System Officers and 76 System Assistants).		LAN & H/W Purchase Order needs to be issued for the 6 Districts.

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
			LAN Survey order for 119 (Taluka) CC's to be issued.
			Proper Training needs to be imparted to the system officers and court staff on CIS Software at the 34 DCs
Orissa	Site preparation to be expedited at the remaining 17 court complexes, which have been funded through NIC/State Govt.	The LAN survey to be completed at 98 court complexes reported as ready by the High Court.	Fund transfer for DG set procurement at 2 court complexes to be taken up.
		Delivery and installation of LAN to be taken up at 2 district court complexes where orders had been issued in Sep'10.	
	Cost estimates to be sent to NIC for site preparation at balance 7 out of 124 court complexes, if required.		
Patna	Funds sent for site preparation at 117 court complexes in Jan 2009 and June 2009 to the High Court by NIC. HC has reported site readiness at only 6 court complexes till date. Pending site preparation to be completed at 111 court complexes.	Computerization work cannot be initiated until the sites are not ready.	
	Site preparation cost estimates for balance 61 /178 court complexes to be sent to NIC HQ.		
Rajasthan	Procurement & Installation of DG set to be completed by March 11 at 38/91 CCs, where no of courts are more than one.	Schedule for Site/LAN survey to be shared for all pending 138 CCs	DG set funds to be send by NIC HQ for 91 CCs where HW/LAN POs has been issued.

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
		HW delivery / installation to be completed at 80 ordered CCs.	PO for Technical manpower (SA) to be issued for 4 District, where HW already installed.
		LAN delivery to be completed at 77 ordered CCs.	
		LAN installation to be completed at 89 ordered CCs.	
Punjab & Haryana	Duly filled Site readiness proformas for the Taluka Courts in Punjab to be sent to NIC HQ.	Hardware / LAN installation to be completed at balance court complexes.	CIS Installation to be expedited at Dist Courts where HW Installation has been completed.
	Pending Technical Manpower (System Assistant Officers) to be recruited and deployed.	HARYANA: Site / LAN survey at 23 taluka CCs to be completed by HP.	
	PUNJAB: The funds for JSC/CSR Site Readiness utilized for Punjab to be conveyed to NIC HQ in confirmation with PWD Punjab for the release of balance funds to PWD Punjab by NIC HQ.	PUNJAB: Site / LAN Survey at 6 Taluka CCs to be started by HP. The schedule for the survey to be provided to the High Court by HP.	
Shimla	DG Set cost estimates to be sent to NIC for all district & taluka CCs.	LAN / HW installation to be taken up at district courts.	LAN Survey reports to be examined and POs to be issued for 30 taluka CCs.
Sikkim	Site preparation cost estimates for 1 CC to be sent to NIC HQ.	N/A	N/A
Uttarakhand	Pending site readiness to be completed.	LAN survey to be completed at 15 ready sites by vendor.	Hardware re-distribution to be worked out for court complexes to utilize excess ordered hardware.
