

eCourts Mission Mode Project

Monthly Project Progress Summary and Key Issues

1 January 2011 - 31 January 2011


Table of Contents

1. Country-wide progress status summary	3
2. High Court wise issues.....	5


1. Country-wide progress status summary

The following two figures show the status of project implementation across the country, as of January 31, 2011. It also shows the increment in the various modules in January.

For the purpose of clarity, the status has been reported in terms of Courts as well as in Court Complexes in figure I and figure II respectively.

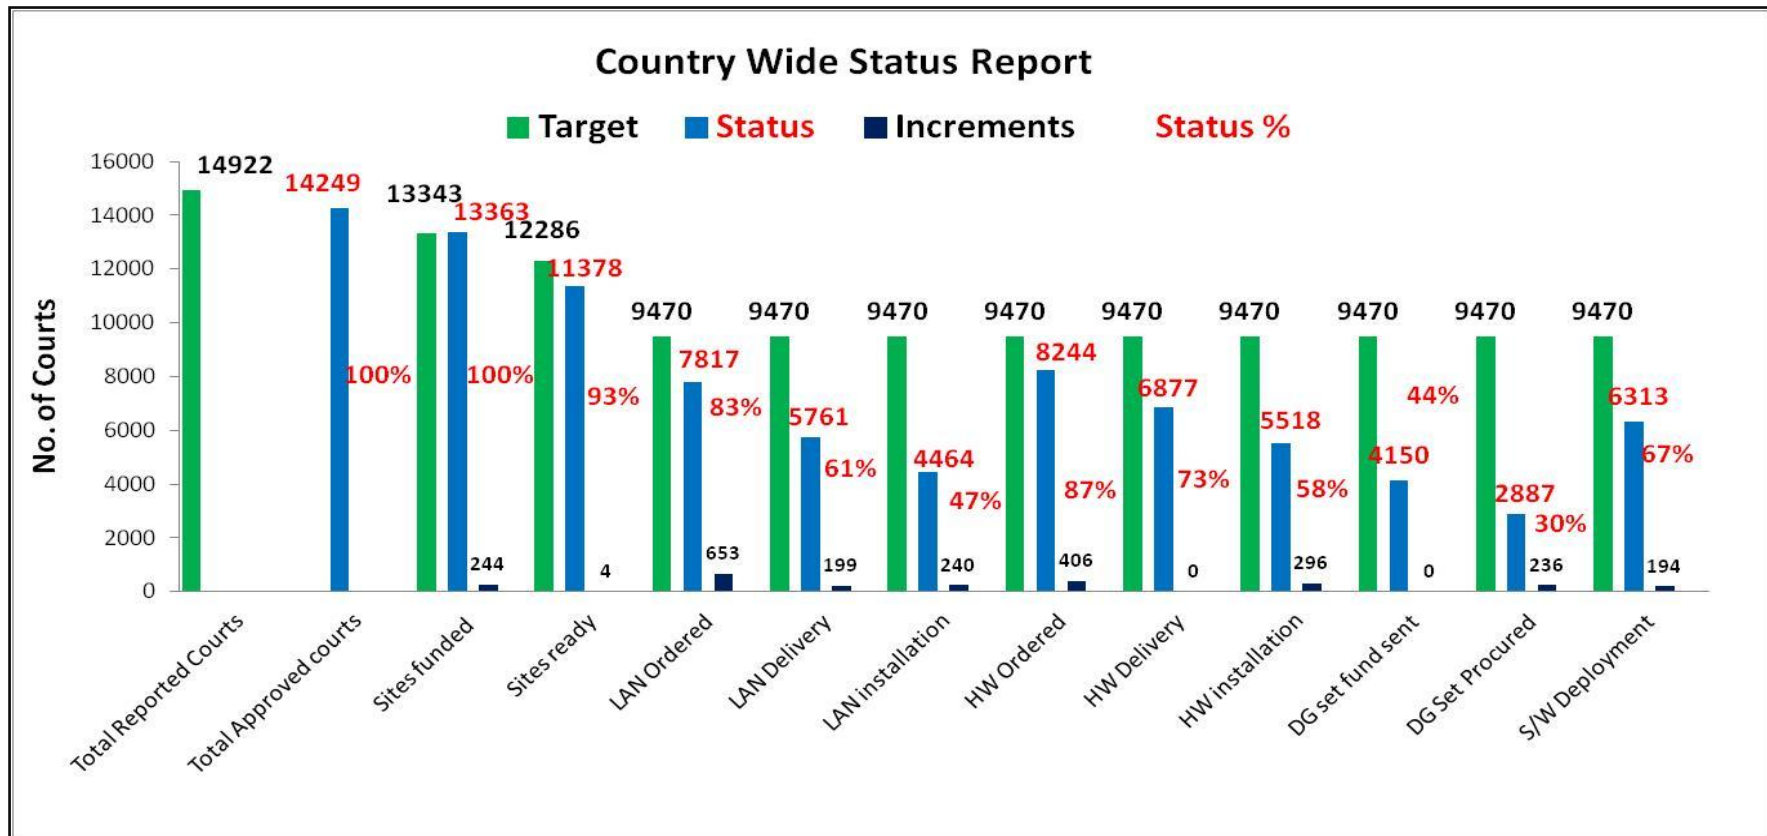

For the Time Period: 1 - 31 January 2011
 Figure I: Country Wide Status Reports (Courts)

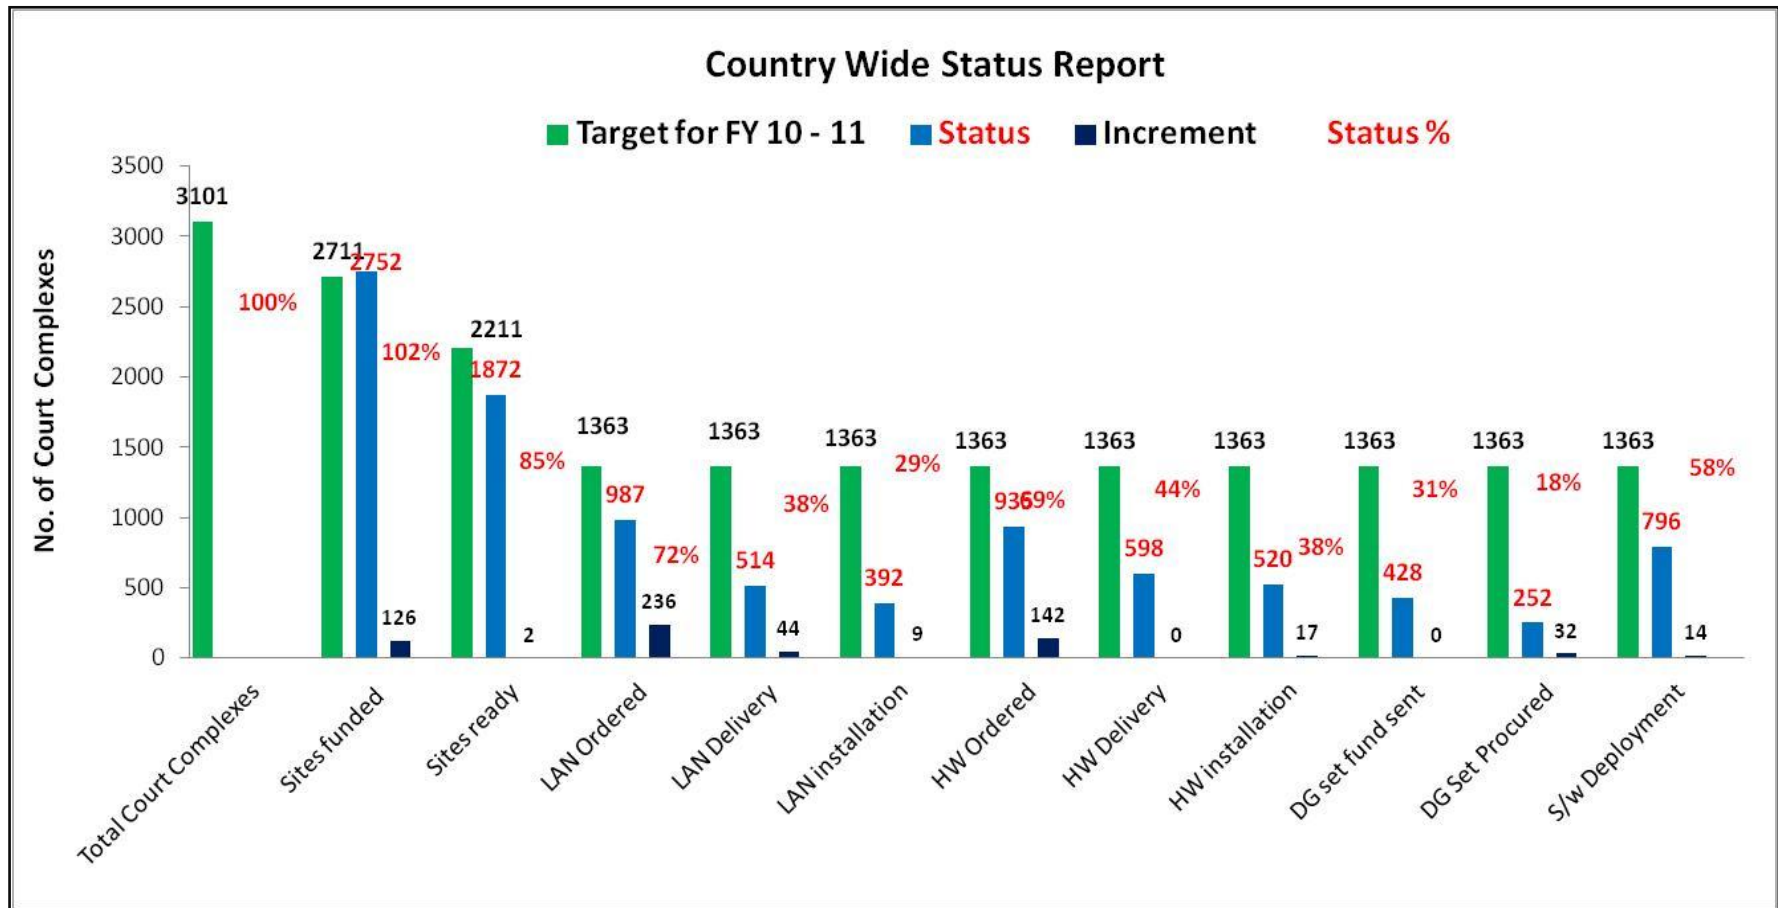

For the Time Period: 1 - 31 January 2011
 Figure II: Country Wide Status Reports (Court Complexes)

2. High Court wise issues

The following list highlights issues in project implementation that need to be addressed by the stakeholders listed.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
1	Allahabad	Sites where installation is halted due to site non readiness to be made ready and handed over to vendor for HW / LAN installation.	To expedite hardware / LAN installation at District CCs (court complexes) - Schedule to be given to NIC / HC.	Stringent monitoring of vendor progress to be done to achieve target completion.
		Cost Estimates for DG Sets to be sent for 70 DCs where HW ordered		
2	AP	Site Preparation activity to be expedited by HC for 237 CCs.	Vendor M/s HCL to take up the LAN Survey at 2 CCs	Fund transfer for DG set procurement at 27 court complexes to be taken up.
		DG set procurement to be expedited by the HC at 9 CCs.	Vendor M/s HCL to initiate delivery and installation of Hardware material at 22 District CCs for which order issued in Nov'10 and Jan'11.	Funds transfer for data entry of pending cases.
		Selection of technical manpower to be taken up by HC	Vendor M/s HCL to initiate delivery and installation of LAN material at 14 CCs for which orders have been issued in Jan'11.	
		Deployment of Application software to be taken up for balance 22 CCs.	M/s Wipro to submit the LAN diagram at High Court for sign-off.	
		Demand Notes for providing connectivity to DCs to be submitted to NIC.		
		Site readiness for HC LAN installation to be given by HC.		

Consolidated Pending Issues Document

S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
3	Bombay	DG sets to be procured at 9/120 CCs, and DG set Installation to be completed at 120 DCC by 31-March-2011	LAN installation to be completed at pending 21 CCs by 15/02/2011	Stringent monitoring of vendor progress to be done to achieve target completion of Hardware and LAN installations
		Completion of site preparation activity at 256 CCs. under jurisdiction of Bombay High court, latest by 31-March-2011	LAN material delivery and installation schedule of 37 DCC to be shared with High Court in priority and installation of the same should be completed at the earliest	
		Stringent monitoring of vendor progress to be done to achieve target completion of Hardware and LAN installations		
		Completion of Technical manpower (SO/SA) recruitment in the pending District Head quarters at the earliest		
4	Calcutta	DG set procurement to be taken up at pending 7 out of 22 district court complexes, for which funds were sent by NIC in March 2010.	Hardware installation to be expedited at 41 taluka court complexes, for which orders were issued in Jan / Feb 2010	Fund transfer for DG set procurement at (56 +1) taluka court complexes pending.
		Site Preparation at Mayabunder taluka court complex to be expedited.	Distribution of excessive LAN material from the Andaman Bench to the Taluka courts in Andaman	Training for CIS application to the Court Staff at Andaman district court complex pending.
		Old / New LAN integration, data migration and court staff training on eCourts application software to be taken up at the remaining 2 / 22 District Court complexes.	LAN installation schedule at 66 taluka court complexes to be provided (orders issued in Sep / Nov 2010	
		Issue of missing LAN material at High Court to be resolved.	To complete the process for issuance of waybill for pendrives to be distributed at all 22	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
			district court complexes.	
		Site not ready Certificate to be provided to the Vendor for UPS delivered at High Court and district court of South 24 Parganas, as readiness of site pending since past seven months.		
		Feedback wrt CIS software to be provided to eCommittee as per feedback obtained from district court complexes during software trial runs.		
5	Chhattisgarh	Site Preparation cost estimates to be sent for 28 Taluka CC	N/A	Funds for DG set for 14 CCs initiated.
				Funds for site preparation at 25 CCs initiated.
				Above to be sent to HC.
6	Gujarat	Gaps pending in 29/41 Sites to be rectified. Revised SRVFs to be submitted.	To expedite LAN survey at 88 ready CCs.	LAN and Hardware PO to be issued for 25 CCs for which LAN Survey Report has been submitted
		Site preparation to be completed at the balance CCs and SRVFs to be submitted to NIC for LAN Survey PO issuance	To provide a LAN and Hardware component delivery and installation schedule for 19 CCs where PO has been issued	DG Set Cost Estimates for 70 CCs to be reviewed and funds to be allocated
		DG Set to be procured at 54 CCs.		
7	Gauhati	Pending site preparation to be completed at 9 CCs where funds already sent.	LAN installation to be completed at 45 CCs. LAN survey to be completed at balance 27 ready CCs.	
8	Jammu & Kashmir	CPC to analyse the feasibility of LAN / HW Installation in the Taluka	Taluka Site/LAN Survey to be completed by HCL in the Jammu Region at 13	To Coordinate with M/s HCL and LAN Committee to finalize

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
		Courts of Kashmir region through some local agency.	sites.	LAN report and submit to NIC HQ.
		CPC to propose an action plan for LAN / HW Material delivery and Installation in the District Courts situated in Leh and Kargil, since the accessibility for these regions is cut off for the most part of the year.	HW/ LAN issues to be resolved at District Courts by M/s WIPRO.	
		To obtain two consolidated demand notes for all District Courts in State i.e, 1 between NIC district Centre and DC Complex and the second one from SWAN PoPs to DC Complexes for an initial period of 1 year. The same needs to be provided to NIC HQ for the approval of needful funds.		
9	Jharkhand	Cost estimates for site preparation to be sent within the approved limit of 2.75 lacs for the ten taluka court complexes pending for site preparation funding.	Vendor to complete hardware and LAN installation at the 27 court complexes for which orders have been issued in July / August 2010.	To regularly monitor vendor for delivery and installation.
			Finalised LAN survey reports to be submitted at NIC HQ for further PO release.	
10	Karnataka	Site Readiness reported at 119 CCs, 6/119 CCs found as NOT ready. Gaps to be rectified.	To expedite LAN survey at ready taluka CCs (83).	HW / LAN POs to be issued for DCs where survey completed.
		DG Set to be procured at 7 CCs.	HW / LAN installation to be completed at DCs.	
11	Kerala	Selection for pending technical manpower to be taken up.	LAN survey to be completed at 77 Taluka CCs	N/A

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
		DG Sets to be procured at all 40 district court complexes.		
12	Madras	Pending site preparation to be completed at taluka level.	Delivery and installation schedules to be shared for recent POs.	NA
		DG Set to be procured at balance 41 district courts complexes.		
		DG set estimates for all district and taluka court complexes, reported as ready, to be forwarded to NIC HQ for fund transfer.		
13	MP	Pending site preparation cost estimates to be sent to NIC (13).	DG sets to be installed at 39 Districts. The process has been delayed because PWD has got approval for cable length of 10 m only while as they require more than that.	DG set funds to be sent for 4 District Court complexes.
		DG sets to be procured at 39 DCs but need to install at those sites.	LAN Survey Schedule to be shared with HC for the purchase order release on 31-12-2010	Approval from e-committee for recruitment of System Assistants (76).
		Technical manpower need to be deployed. (7 System Officers and 76 System Assistants).		LAN & H/W Purchase Order needs to be issued for the 6 District court complexes.
				Training to be imparted to the system officers and court staff on CIS Software at the 42 District Courts.
				The extra funds approval, Rs.2.65 lakhs pending with NIC for installation of DG Sets.
14	Orissa	Site preparation to be expedited at the remaining 17 court complexes, which have	The LAN survey to be completed at 98 court complexes reported as ready by the High Court.	Fund transfer for DG set procurement at 2 court complexes to be taken up.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
		been funded through NIC/State Govt.		
		Cost estimates to be sent to NIC for site preparation at balance 7 out of 124 court complexes, if required.	Vendor to complete the installation of LAN at Cuttack & Balasore CCs.	
		Electrical Site readiness of to be ensured at Cuttack Court Complex, for completion of LAN installation at Civil Court Complex at Cuttack		
15	Patna	Funds sent for site preparation at 117 court complexes in Jan 2009 and June 2009 to the High Court by NIC. HC has reported site readiness at only 6 court complexes till date. Pending site preparation to be completed at 111 court complexes.	Computerization work cannot be initiated until the sites are ready.	
		Site preparation cost estimates for balance 61 /178 court complexes to be sent to NIC HQ.		
16	Rajasthan	Procurement & Installation of DG set to be completed by March 11 at 108 CCs, once fund will be transferred by NIC HQ to High Court.	M/s. HCL to expedite the Site/LAN survey for remaining 98 CCs and submit the LAN survey report to SLC, where LAN survey already completed.	DG set funds to be transferred by NIC HQ to High Court for 108 CCs.
			HW delivery / installation to be completed by March 11 at ordered Court complexes.	
			M/s. HCL to expedite the LAN installation process for 9 CCs.	
			LAN delivery and installation to be completed by March 11 at all ordered CCs.	

Consolidated Pending Issues Document

S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
17	Punjab & Haryana	PUNJAB, HARYANA, CHANDIGARH: Pending Technical Manpower (System Assistant Officers) to be recruited and deployed.	M/s New Horizons & M/s Pioneer to coordinate with NIC HQ and CPC to finalize the interview schedule.	
		During the Site Survey, M/s HP has found that some courts will be shifted to new location. CPC to share the status update with NIC HQ wrt the schedule of the Sites where the courts are to be shifted in new buildings soon. These sites may be provided SNR Status for March 2011 targets	PUNJAB: Site / LAN survey at 42 CCs to be completed by M/s HP. The schedule for the survey to be provided to the High Court by M/s HP.	To coordinate with CPC and LAN Committee to finalise the LAN reports & submission to NIC HQ.
		To obtain two consolidated demand notes for all District Courts in State i.e, 1 between NIC district Centre and DC Complex and the second one from SWAN PoPs to DC Complexes for an initial period of 1 year. The same needs to be provided to NIC HQ for the approval of needful funds.	PUNJAB: Hardware / LAN installation to be completed at balance court complexes by WIPRO.	To coordinate with CPC for follow up with the SWAN implementing agencies in Punjab, Haryana and Chandigarh to establish SWAN connectivity at the Courts.
		To finalize the Data Entry Plan for the District & Subordinate Courts and share the same with NIC HQ for approval of needful funds.	M/s HP to expedite the delivery of the HW Material at Karnal, Kurukshetra, Kaithal, Yamuna Nagar Districts of Haryana. This PO was issued on 19 Oct 2010.	CIS Installation to be expedited at Dist Courts where HW Installation has been completed.
18	Shimla	DG Set cost estimates to be sent to NIC for all district & taluka CCs, as per the circulated guidelines with required PWD officials' signatures.	LAN / HW installation to be taken up at district courts.	LAN / HW POs initiated for 28 taluka CCs. PO will be issued soon.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor (State Coordinator)	NIC (State Coordinator)
19	Sikkim	Site preparation cost estimates for 1 CC to be sent to NIC HQ.	PWD to expedite site preparation for 3 CCs.	N/A
20	Uttarakhand	Pending site readiness to be completed.		Hardware re-distribution to be worked out for court complexes to utilize excess ordered hardware.
		Decision on computerization of the court complexes running in the rented building, to be conveyed to eCommittee and NIC HQ, as per discussion in the CPC Meeting held on 8 Jan 2011.		
