

eCourts Mission Mode Project

Monthly Project Progress Summary and Key Issues


1 March 2011 - 31 March 2011

Table of Contents

1. Country-wide progress status summary	3
2. High Court wise issues.....	55


1. Country-wide progress status summary

The following two figures show the status of project implementation across the country, as of March 31, 2011. It also shows the increment in the various modules in March. For the purpose of clarity, the status has been reported in terms of Courts as well as in Court Complexes in figure I and figure II respectively.

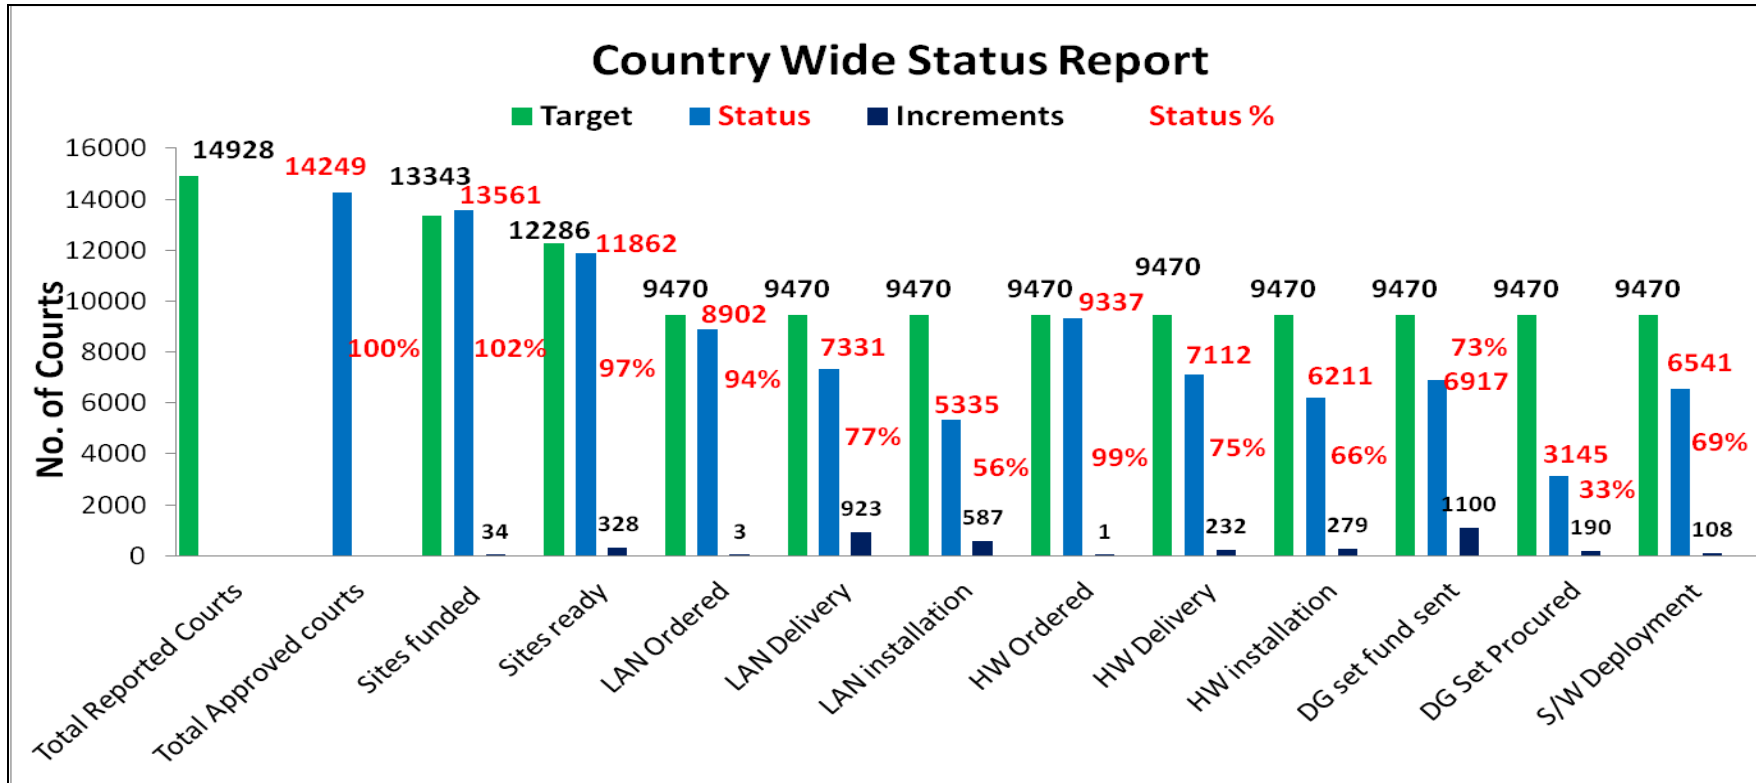

For the Time Period: 1 - 31 March 2011

Figure I

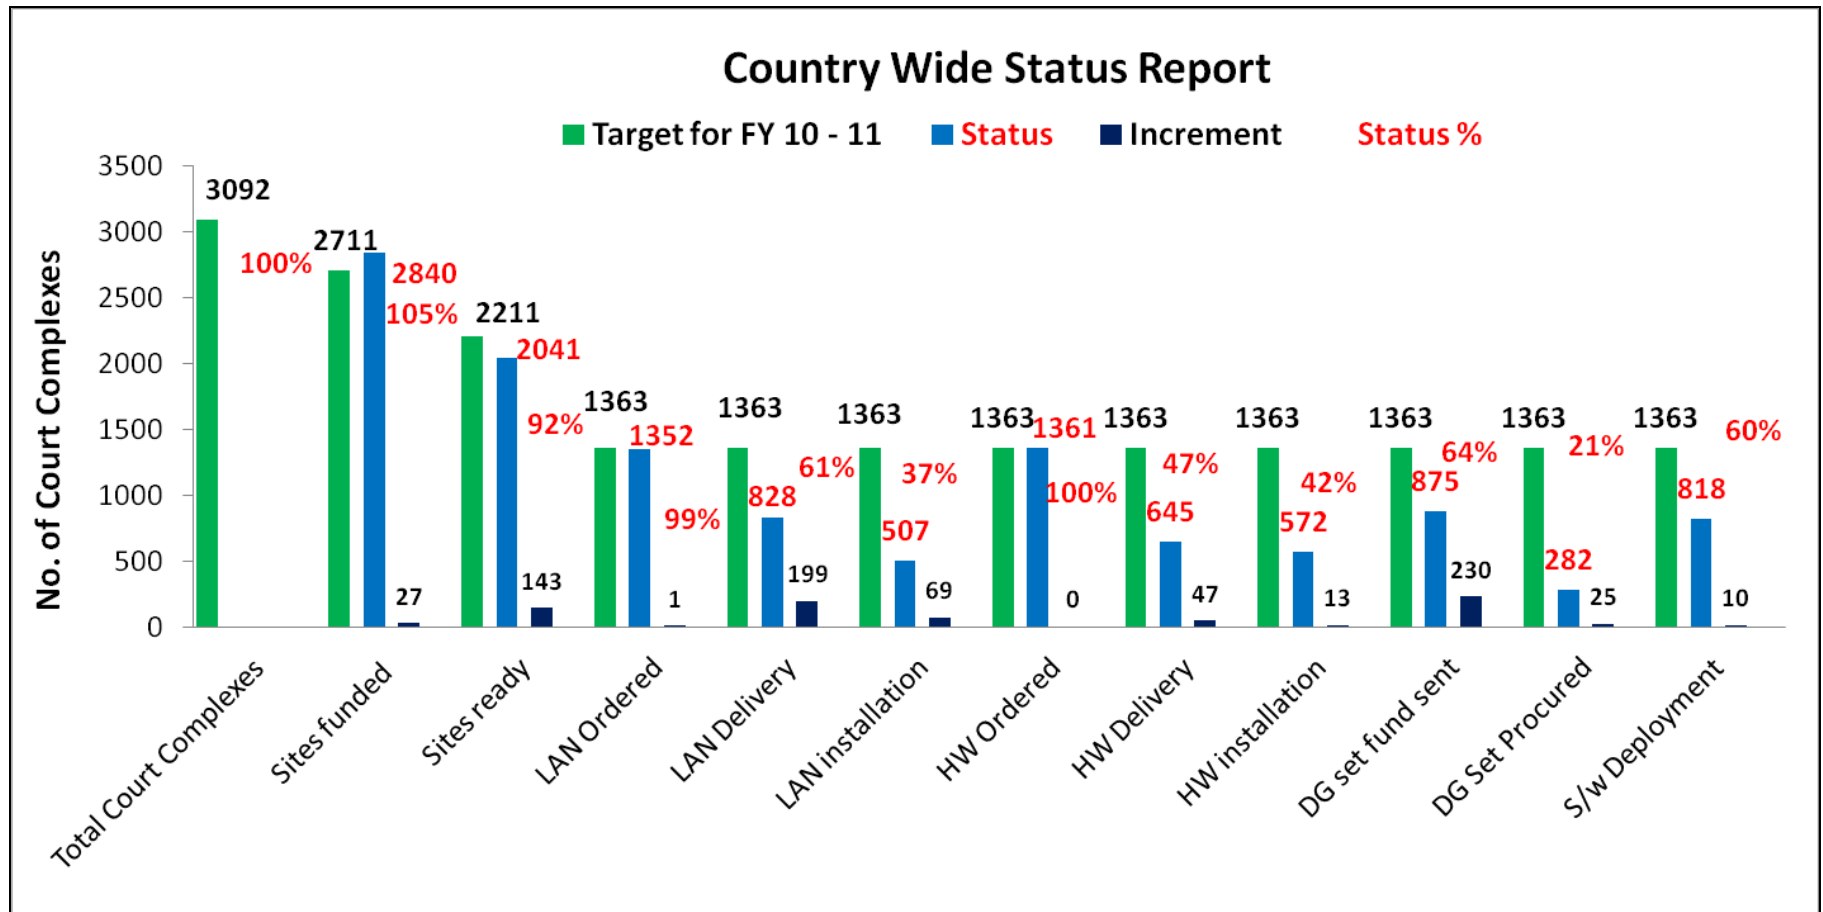

For the Time Period: 1 - 31 March 2011

Figure II

2. High Court wise issues

The following list highlights issues in project implementation that need to be addressed by the stakeholders listed.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
1	Allahabad	Sites where installation is halted due to site non-readiness. Sites are to be made ready and have to be handed over to vendor for hardware and LAN installation.	To expedite hardware / LAN installation at District court complexes - Schedule to be given to NIC and HC.	Stringent monitoring of vendor progress to be done.
		Demand notes for WAN connectivity at the District HQ which are to be obtained from BSNL and further need to be sent to NIC HQ.	Vendor to take up the commitments made in the meeting held in Supreme Court of India on 29 Jan 2011.	NIC to resolve CIS software problem.
		To expedite hardware and LAN installation at District court complexes.	Complaints / Issues pending resolution from HCL regarding hardware and LAN to be resolved.	
2	Andhra Pradesh	Site Preparation activity to be expedited by HC for 220 CCs.	Vendor M/s HCL to expedite installation of Hardware material at 8 locations where material has been delivered.	Funds for data entry of pending cases is sanctioned at NIC HQ and transfer to to HC be done by the bank.
		DG set procurement to be expedited by the HC at 25 CCs.	Vendor M/s HCL to expedite delivery of Hardware material at 4 locations is delivered partially, and 10 locations where no deliver of material is recorded.	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		Deployment of Application software to be taken up for balance 7 CCs.	Vendor M/s HCL to initiate installation of LAN material at 12 locations where material has been delivered.	NIC HQ to review /approve and release of PO for supply and installation of LAN and HW material at 2 locations for which LAN survey reports have been submitted to NIC HQ by vendor M/s HCL.
		Data entry plan of the pending cases to database to be sent to NIC.	Vendor M/s HCL to expedite delivery of LAN material at 2 locations.	
		Deployment of Technical Manpower - System Assistants		
3	Bombay	DG sets to be procured at remaining 2 CCs. Fund utilization certificates of DG sets to be sent to NIC, HQ at the earliest.	Vendor M/s HCL was unable to complete the pending 8 LAN installation work by 31/03/2011; the same need to be completed at the earliest. Schedule to be shared for same.	Stringent monitoring of vendor progress to be done to achieve target completion of Hardware and LAN installations
		Site Preparation activity to be expedited by HC for 138 CCs. under jurisdiction of Bombay High Court.	Vendor M/s HCL to initiate installation of LAN material at 34 locations where material has been delivered.	Software to be updated with Marathi language support. NIC coordinator to discuss

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
				with CPC and revert to NIC HQ on the committed completion date.
		High Court to submit SRVFs in batches so that LAN and HW orders can be issued for ready sites	Vendor M/s HCL to expedite delivery and installation of Hardware material at 2 locations	
		Stringent monitoring of vendor progress to be done to achieve target completion of Hardware and LAN installations		
		Deployment of Application software with Marathi language support to be taken up for all court complexes		
	Bombay	Plan for data entry to be completed and communicated to all concerned.		
4	Calcutta	DG set procurement to be taken up at pending 6 out of 22 district court complexes, for which funds were sent by NIC in March 2010.	LAN installation to be complete at all 66 taluka court complexes, were installation was scheduled to be completed by March, 2011	Training for CIS application to the Court Staff at Andaman district court complex pending.
		Site Preparation at Mayabunder taluka court complex to be expedited.	Distribution of excessive LAN material from the Andaman Bench to the taluka courts in Andaman	Feedback wrt CIS software provided by the High Court Software Feedback Committee to be incorporated

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
				in the CIS software
		Old / New LAN integration, data migration and court staff training on eCourts application software to be taken up at the remaining 2 / 22 district court complexes.	Delivery and installation of hardware material at 23 taluka court complexes for which order was issued in December, 2010 to be completed	Feedback provided for the backlog entry module to be incorporated in the CIS software
		Issue of missing LAN material at High Court to be resolved.		UPS at district court of South 24 Parganas to be recalled
		Site not ready Certificate to be provided to the Vendor for UPS delivered at High Court.		
5	Chhattisgarh	Site preparation work to be completed at Janjgir (Champa) court complex.	Servers to be delivered at Dantewada and Dhamtari districts by M/s HP.	
		Site preparation to be taken up at the 46 court complexes where funds have been sent to the HC.	Issues with OFC cable to be rectified by M/s Wipro at Bilaspur and Durg districts.	Centralized CIS Software to be deployed at District courts.
		Plan for data entry to be completed and communicated to all concerned.	LAN survey to be done for Uttar Bastar (Kanker) court complex by M/s HP.	
			M/s Pioneer e-labs Ltd. to return security deposit to Technical Manpower.	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
6	Gujarat	Gaps in site readiness (electrical points) rectified in 30 / 41 CCs; rectification in progress in 3 CCs, and pending at 8 CCs. These to be completed soon. Revised SRVFs to be submitted to NIC HQ.	LAN Survey completed in 21 CCs. Report of 15 CCs pending for submission to HC by M/s HP.	LAN Survey job order to be issued by NIC HQ for 24 Court Complexes for which Site Readiness Verification Forms have been submitted.
		Site Preparation for pending 26 CCs which are functioning in rented premises is being reviewed by HC committee. Permission granted to 3 CCs for site preparation which have moved to new premise. Decision on rest to be communicated to NIC HQ.	LAN Survey schedule for pending 44 CCs submitted. Survey to last till 15th May 2011. Vendor to provision additional resources to compress the schedule	Clarification required on the technical manpower funds proposed to be transferred to HC
		Purchase Order issued for procurement of 65 DG Sets to M/s. Elmech Engineers on 31/3/2011. Vendor has committed to complete supply and commissioning with 3 months	LAN component delivery schedule for 19 CCs for which material inspection at NIC is proposed on 5th April to be submitted to HC	
		Preliminary Meeting undertaken with DST and BSNL to define the 8 Mbps WAN connectivity requirement.	Hardware Delivery Schedule to be provided for 110 CCs	
		Details of pending 3-4 lac cases for Data-entry to be consolidated for	LAN component inspection and delivery schedule for 91 CCs to	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		submission to NIC	be provided	
7	Gauhati	Site Readiness at balance 23 court complexes to be completed on priority - Tripura -6, Assam - 2, Mizoram - 1, Manipur - 14.	H/W material not received for 37/52 CCs and LAN material not received for 28 / 55 CCs.	
			VC equipment yet to be installed at HC Benches other than Shillong Bench.	
8	MP	Pending site preparation cost estimates to be sent to NIC (13).	LAN & H/W Purchase Order needs to be issued for the 6 District court complexes.	Training to be imparted to the system officers and court staff on CIS Software at the 42 District Courts.
		DG sets to be installed at 39 Districts. The process has been delayed because PWD has got approval for cable length of 10 m only while as they require more than that.		The extra funds, Rs.2.65 sanctioned by NIC for installation of DG Sets.
9	Jammu & Kashmir	To analyze the feasibility of LAN / HW Installation in the Taluka Courts of Kashmir region through some local agency.	To Coordinate with M/s HCL and LAN Committee to finalize LAN report and submit to NIC HQ.	
		To propose an action plan for LAN / HW Material delivery and Installation in the	M/s WIPRO to provide LAN / HW Support at the Dist Sites; complaints to be	N/A

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		District Courts situated in Leh and Kargil, since the accessibility for these regions is cut off for the most part of the year.	resolved.	
		To obtain two consolidated demand notes for all WAN Connectivity provision at District.	M/s HCL to submit the tentative LAN / HW installation plan for Taluka Sites in the Jammu Region to CPC / NIC Coordinator.	To coordinate with CPC for follow up with the SWAN / NICNET implementing agencies in JK to establish WAN connectivity at the Courts.
10	Jharkhand	Cost estimates for site preparation to be sent within the approved limit of 2.75 lacs for 10 taluka court complexes pending for site preparation funding.	Vendor to complete hardware and LAN installation at the 58 court complexes for which orders have been issued in July / August 2010 & 2011.	NIC to regularly monitor vendor for delivery and installation.
		DG Set procurement and installation to be initiated.		Regarding website NIC will communicate to Jharkhand.
11	Rajasthan	Procurement & Installation of DG set to be completed at 108 CCs.	M/s. HCL to discuss the LAN survey report for 40 CCs to NIC HQ, where LAN survey already completed and approved by SLC, Jaipur	NIC to send the S/w installation team at Jaipur District Court Complex.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		Software to be deployed at Jaipur District CC, as LAN installation completed at Jaipur DC. Expected on 7-8 Apr 2011.	HW delivery / installation to be completed at ordered Court complexes.	
		Plan for data entry to be completed and communicated to all concerned.	M/s. HCL to expedite the LAN installation process at remaining sites where LAN items already delivered.	
12	Karnataka	Plan for data entry to be completed and communicated to all concerned.	Schedule for Site/LAN survey at 8 locations where work order was issued.	Funds to be released to PWD for 8 sites for which estimates have been submitted.
		Estimates for DG sets at taluka sites to be submitted.	HW delivery / installation to be completed at District and Taluka courts.	Funds for 4 special cases where site preparation activities cannot be taken up but LAN/HW alone required.
		Site Preparation to be completed at the remaining taluka sites by PWD.		LAN Survey Order to be issued for 6 Court Complexes for which Site Readiness Verification Forms have been submitted
13	Kerala	Selection for pending technical manpower to be taken up.	LAN installation to be completed at 65 Taluka court complexes (CCs)	N/A

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		DG Sets to be procured at all 40 district court complexes.	Hardware delivery to be initiated for the 77 court complexes.	
		Site preparation to be completed in 3 court complexes at Lakshadweep.		
		Demand notes for the WAN connectivity to be submitted.		
14	Madras	Pending site preparation to be completed at talukka level.	submission of BOM documents to be completed for 18 court complexes - M/s HP.	Installation of L3 switches have to be completed.
		DG Set to be procured at balance 31 district courts complexes.		Addl. Hardware for 21 district courts complexes to be processed.
		DG set cost estimates for 5 district CC and 17 taluka CC, reported as ready, have to be forwarded to NIC HQ for fund transfer.		Addl site preparation funds requests for 3 cc to be processed.
		WAN Connectivity demand notes to be forwarded by the HC.		
15	Orissa	Site preparation to be expedited and SRVF to be provided for the remaining 14 court complexes, which have been funded through NIC/State Govt.	Actual LAN survey report to be submitted for 34 of 66 taluka court complexes where survey has been completed	Delivery of LAN switches at the Districts of Balasore and Cuttack by NICS I
		DG set estimates sent for two single Court Complexes at Berhampur and Bhawanipatna to be returned to the NIC HQ	Delivery and installation of LAN material at 32 court complexes to be completed for which order was issued in	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
			Jan/Feb 2011	
			The LAN survey to be completed at remaining 32 of 98 court complexes reported as ready by the High Court.	
16	Patna	Funds sent for site preparation at 117 court complexes in Jan 2009 and June 2009 to the High Court by NIC. HC has reported site readiness at only 24 court complexes till date. Pending site preparation to be completed at 93 court complexes.	21 Sites LAN survey order issued. 17/21 reports pending.	
		Site preparation cost estimates for balance 61/178 court complexes to be sent to NIC HQ.		
17	Punjab & Haryana	Site issues reported by M/s HP based on Site Survey to be taken up with PWD. Gaps to be resolved in coordination with PWD.	M/S HP to share the issues with CPC on priority.	CIS Installation to be expedited at Dist Courts where HW Installation has been completed - 8 locations - NIC HQ and NIC state to plan.

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
		To coordinate with M/s WIPRO for the LAN / HW Installation Completion at all 29 Dist Courts. Coordinate with DSJs to facilitate the HW Installation Sign Offs.	M/s WIPRO to complete the HW / LAN installation at balance Dist Sites.	Coordinate with DIOs to facilitate the LAN / HW Installation Sign Offs.
		Pending Technical Manpower (System Assistant Officers) to be recruited and deployed on priority.	M/s WIPRO to provide support for LAN / HW Complaints resolution on priority, since sign offs are pending because of pending HW Complaints.	To coordinate with CPC for follow up with the SWAN / NICNET implementing agencies in Punjab, Haryana and Chandigarh to establish SWAN connectivity at the Courts.
		WAN Connectivity demand notes pending from BSNL.	M/S HP to share the LAN /HW Material delivery / installation schedule with CPC urgently for Punjab and Haryana for the sites committed for computerization by March 2011.	To confirm LAN / HW PO cancellations required to NIC HQ for Panipat and 8 sites of Punjab where LAN is already available.
17	Punjab and Haryana	PUNJAB: To confirm the installation of ACs at the JSC in Punjab; share the fund utilization certificate with NIC HQ	M/s HP to expedite the delivery of the HW Material at Karnal, Kurukshetra, Kaithal, Yamuna Nagar District Courts. This PO was issued on 19 Oct 2010.	

Consolidated Pending Issues Document				
S.No	HC	Judiciary(CPC)	Vendor	NIC
18	Shimla	DG set procurement to be initiated	LAN / HW installation to be taken up at district / taluka courts and implementation schedule to be given by M/s HP.	
		Data entry plan to be formulated and be shared with NIC HQ.		
19	Sikkim	Pending site preparation to be completed at 3 CCs where funds already sent.	NA	NA
		PWD to expedite and send site preparation cost estimate of balance 1 sites to NIC HQ.		
20	Uttarakhand	Decision on computerization of the court complexes running in the rented building, to be conveyed to eCommittee and NIC HQ, as per discussion in the CPC Meeting held on 8 Jan 2011.	Hardware redistribution to be taken up by M/s Wipro.	
		Plan for data entry to be shared with NIC HQ.	LAN and HW item delivery and installation schedule to be given by M/s HP and work to be expedited.	Funds for data entry have been sanctioned and to be transferred to the HC.
