

eCourts Mission Mode Project

Monthly Project Progress Summary and Key Issues

1 November 2010 - 30 November 2010


Table of Contents

- 1. Country-wide progress status summary 3
- 2. High Court wise issues..... 5


1. Country-wide progress status summary

The following two figures show the status of project implementation across the country, as of November 30, 2010. It also shows the increment in the various modules in November.

For the purpose of clarity, the status has been reported in terms of Courts as well as in Court Complexes in figure I and figure II respectively.

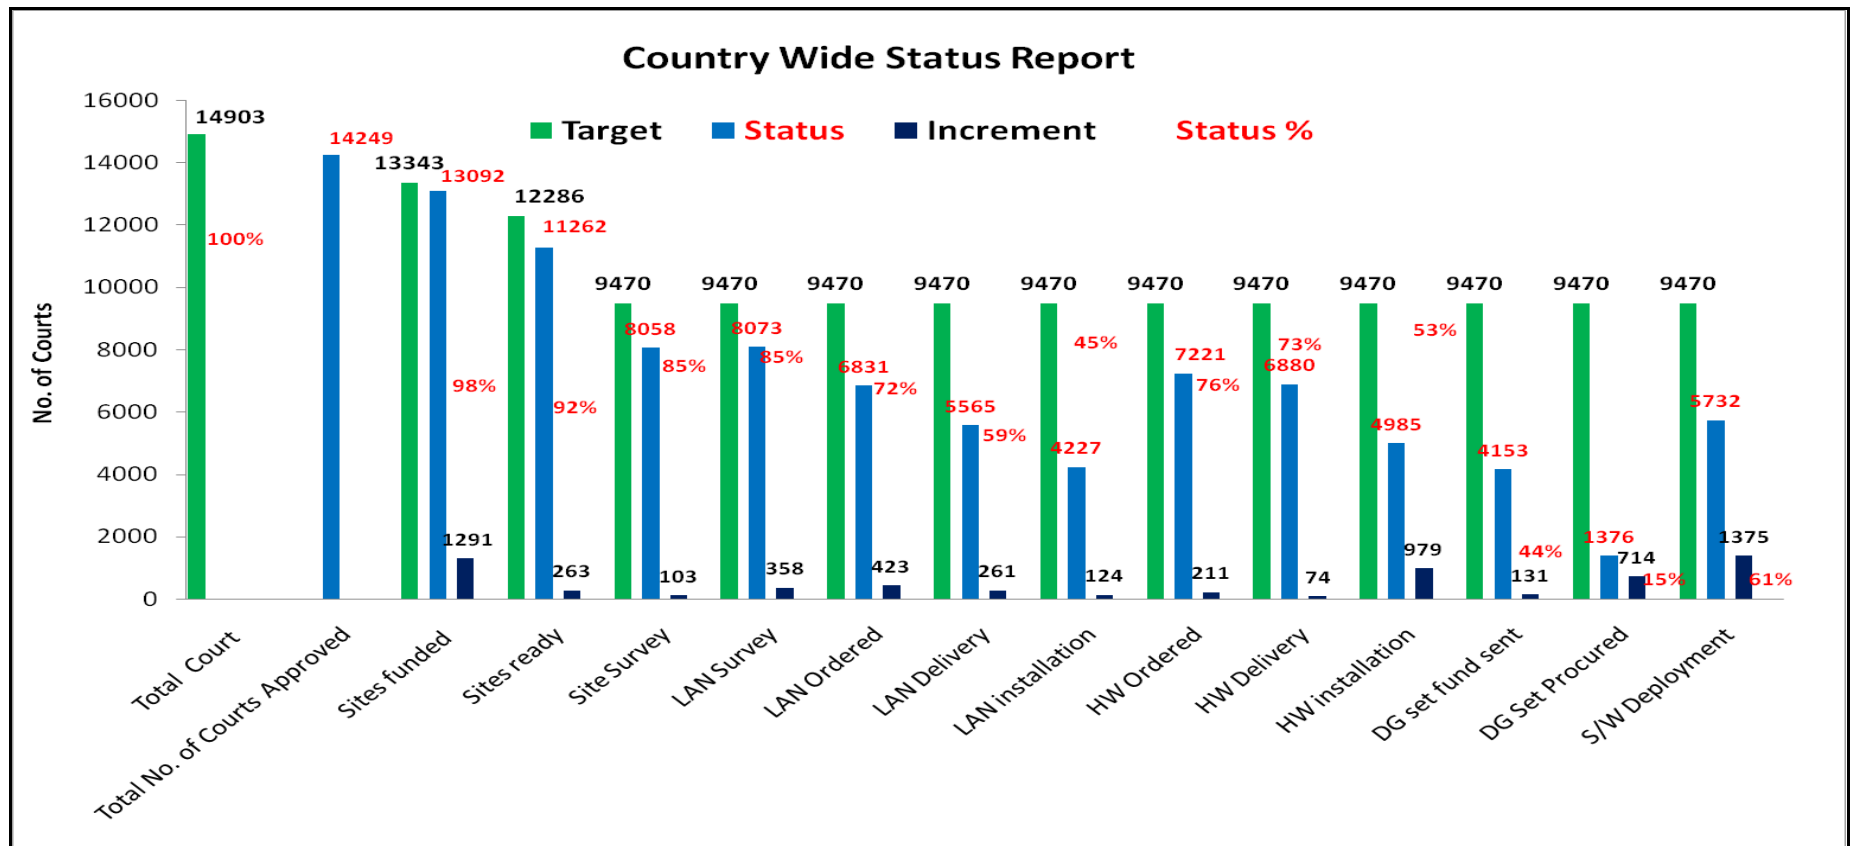

For the Time Period: 1 - 30 November 2010
 Figure I: Country Wide Status Reports (Courts)

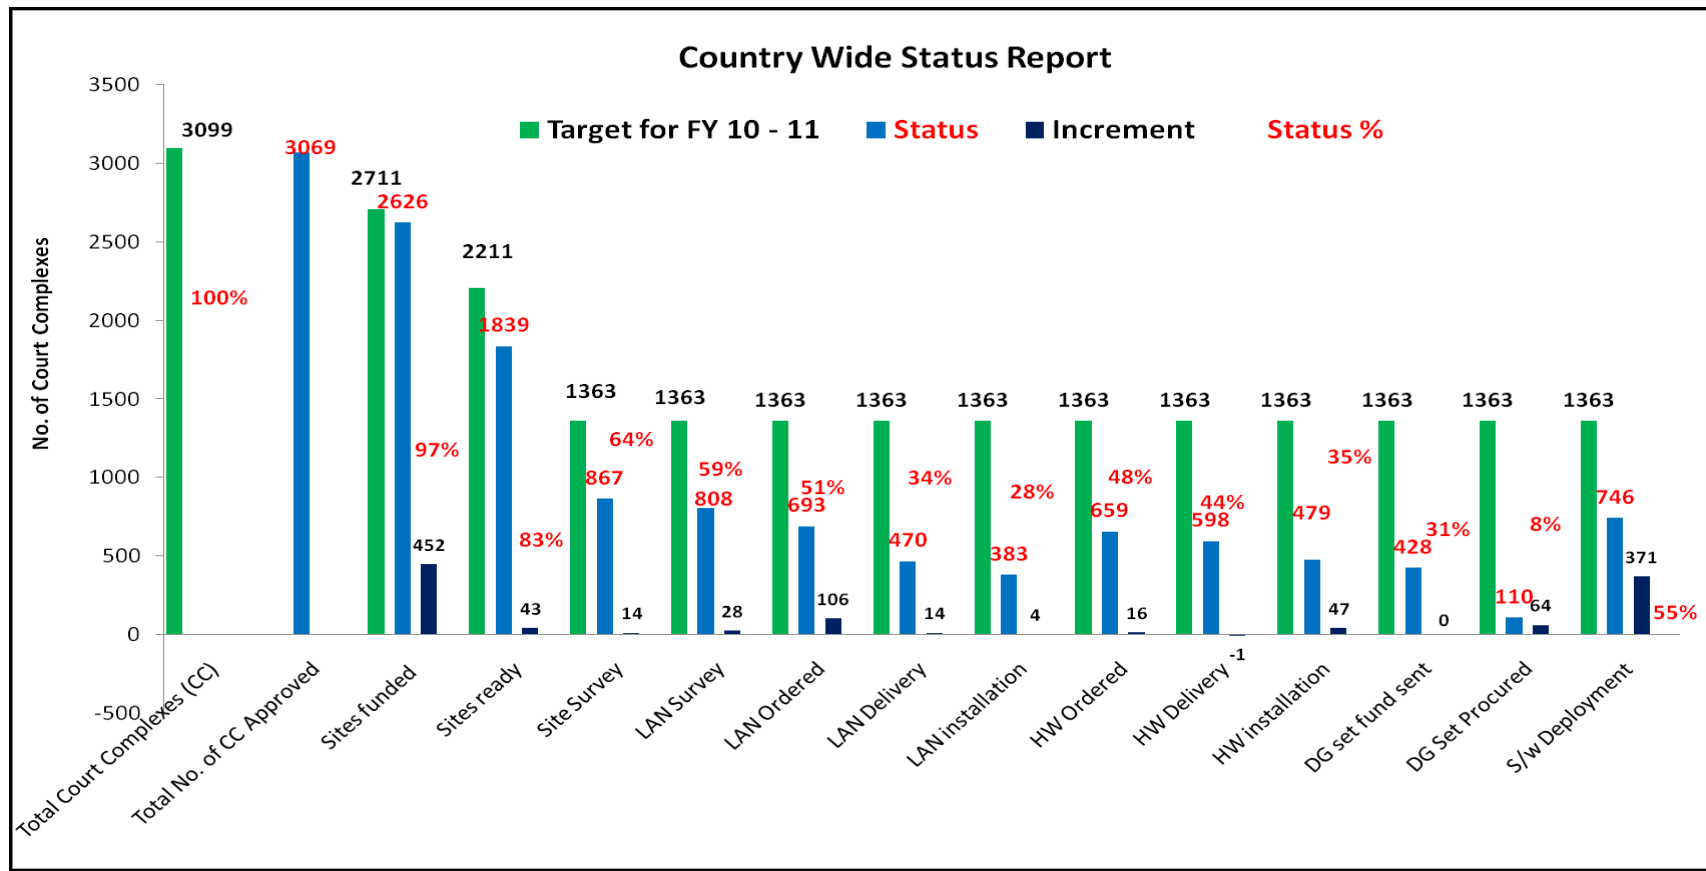

For the Time Period: 1 - 30 November 2010
Figure II: Country Wide Status Reports (Court Complexes)

2. High Court wise issues

The following list highlights issues in project implementation that need to be addressed by the stakeholders listed.

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
Allahabad	Sites where installation is halted due to site non readiness to be made ready and handed over to vendor for HW / LAN installation.	To expedite hardware / LAN installation at District CCs (court complexes) - Schedule to be given to NIC.	Stringent monitoring of vendor progress to be done to achieve target completion.
	Cost Estimates for DG Sets to be sent for 70 DCs where HW ordered		
AP	Site Preparation activity to be expedited by HC for 237 CCs.	Vendor M/s HCL to take up the LAN Survey at 2 CCs.	Funds to be transferred for DG sets for pending 11 CCs.
	DG set procurement to be expedited by the HC at 9 CCs.		
	Selection of technical manpower to be taken up by HC.	Vendor M/s HCL to initiate delivery and installation of Hardware material at 8 District CCs.	LAN Installation orders for 16 CCs to be initiated.
	Deployment of Application software to be taken up for balance 22 CCs.		
	Site readiness for HC LAN installation to be given by HC.		
Bombay	DG sets to be procured at 120 CCs.	LAN installation to be completed at pending 22 CCs.	Fund Transfer to be done for site preparation at 169 CCs.
	Initiation of site prep. work at 217 CCs.	LAN survey to be completed at 34 CCs where HW PO issued.	
Calcutta	DG set procurement to be taken up for pending district courts.	Hardware installation to be expedited in 41 Talukas.	
	Site Preparation of the Andaman Bench to be expedited.	LAN material delivery and installation to be started at 63 Talukas.	

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
	LAN integration and migration and training, feedback of CIS software to be taken up for the remaining 3 DCs.		
Chhattisgarh	Site Preparation cost estimates to be sent for 44 taluka court complexes.	N/A	Funds for DG set for 14 CCs initiated.
			Funds for site preparation at 25 CCs initiated.
			Above to be sent to HC
Gauhati	Pending site preparation to be completed at 12 CCs where funds already sent.	LAN installation to be completed at 29 CCs.	HW POs to be issued for 13 CCs where LAN PO issued recently.
		LAN survey to be completed at balance 26 ready CCs.	
Gujarat	Site Readiness reported at 107 CCs, 41/107 CCs found as NOT ready - Gaps to be rectified.	To expedite LAN survey at 40 ready CCs.	N/A
	Site preparation to be completed at the balance CCs.		
	DG Set to be procured at 54 CCs.		
Jammu & Kashmir		Taluka Site/LAN Survey to be started.	SW installation to be expedited.
		HW/ LAN Installation to be expedited at District Courts.	
Jharkhand	Cost estimate for site prep to be sent for 2.75 lacs fr the ten talukas	Vendor to complete Hardware and LAN installation at 27 ready CCs	
Karnataka	Site Readiness reported at 119 CCs, 13/119 CCs found as NOT ready. Gaps to be rectified.	To expedite LAN survey at ready taluka CCs (83).	HW / LAN POs to be issued for DCs where survey completed.
	DG Set to be procured at 7 CCs.	HW / LAN installation to be completed at DCs.	
Kerala	Selection for pending technical manpower to be	LAN survey to be initiated at Taluka	N/A

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
	taken up.	CCs.	
	DG Sets to be procured at all 40 district court complexes.		
Madras	Pending site preparation to be completed at taluka level.	LAN Survey and submission of BOM documents to be completed for 90 court complexes - HP.	L3 switches delivery pending for 4 district Court complexes.
	DG Set to be procured at balance 43 district courts complexes.	LAN installation pending for two courts- Wipro.	
	DG set estimates for taluka court complexes to be forwarded to NIC HQ.		
MP	Pending site prep. cost estimates to be sent to NIC (13).	LAN Survey to be completed at 6 Districts court complexes.	DG set funds to be sent for 4 DCs.
	Site Readiness reported at 119 CCs, 68/119 CCs found as NOT ready. Gaps to be rectified.		LAN Survey order for 51 CC's to be issued.
	DG set to be procured at DCs (39).		Approval from e-committee for recruitment of SA.
	Technical manpower to be deployed.		
Orissa	Site preparation to be expedited for the remaining 23 Court Complexes	The LAN survey to be expedited for 98 Court Complexes	Fund for DG set to be released for 2 District CCs
		Delivery of LAN material to be made for 2 District CCs	
Patna	Pending site preparation to be completed at 111 court complexes.	N/A	N/A
	Site preparation cost estimates for balance CCs to be sent to NIC HQ.		
Punjab & Haryana at Chandigarh	Gaps in taluka site readiness in Punjab to be rectified by the HC and site readiness proformas to be sent to NIC.	Hardware / LAN installation to be completed at balance court complexes.	N/A

HC	Judiciary (CPC)	Vendor (State coordinator)	NIC (State coordinator)
	Pending Technical Manpower to be recruited and deployed.	LAN survey at 23 taluka CCs in Haryana to be completed, LAN Survey at Taluka CCs in Punjab to be started.	
Rajasthan	N/A	LAN surveys at 133 CCs to be completed.	Pending HW orders to be placed for 55 CCs where LAN has been recently ordered.
		HW delivery / installation to be completed at 3 ordered CCs.	
		LAN delivery to be completed at 58 ordered CCs.	LAN PO to be issued at 30 CCs where survey completed.
		LAN installation to be completed at 66 ordered CCs.	
Shimla	DG Set cost estimates to be sent to NIC for all district & taluka CCs.	LAN / HW installation to be taken up at district courts.	LAN Survey reports to be examined and POs to be issued for 30 taluka CCs.
Sikkim	Site preparation cost estimates for 1 CC to be sent to NIC HQ.		
Uttarakhand	Pending site readiness to be completed.	LAN survey to be completed at 15 ready sites by vendor.	Hardware re-distribution to be worked out for court complexes to utilize excess ordered hardware.
