

eCourts MMP


Project Status Presentation

22 September 2010

Agenda

1. Status Summary
2. Progress in implementation in last fortnight
3. HC Wise Project Status and Issues

Status Summary

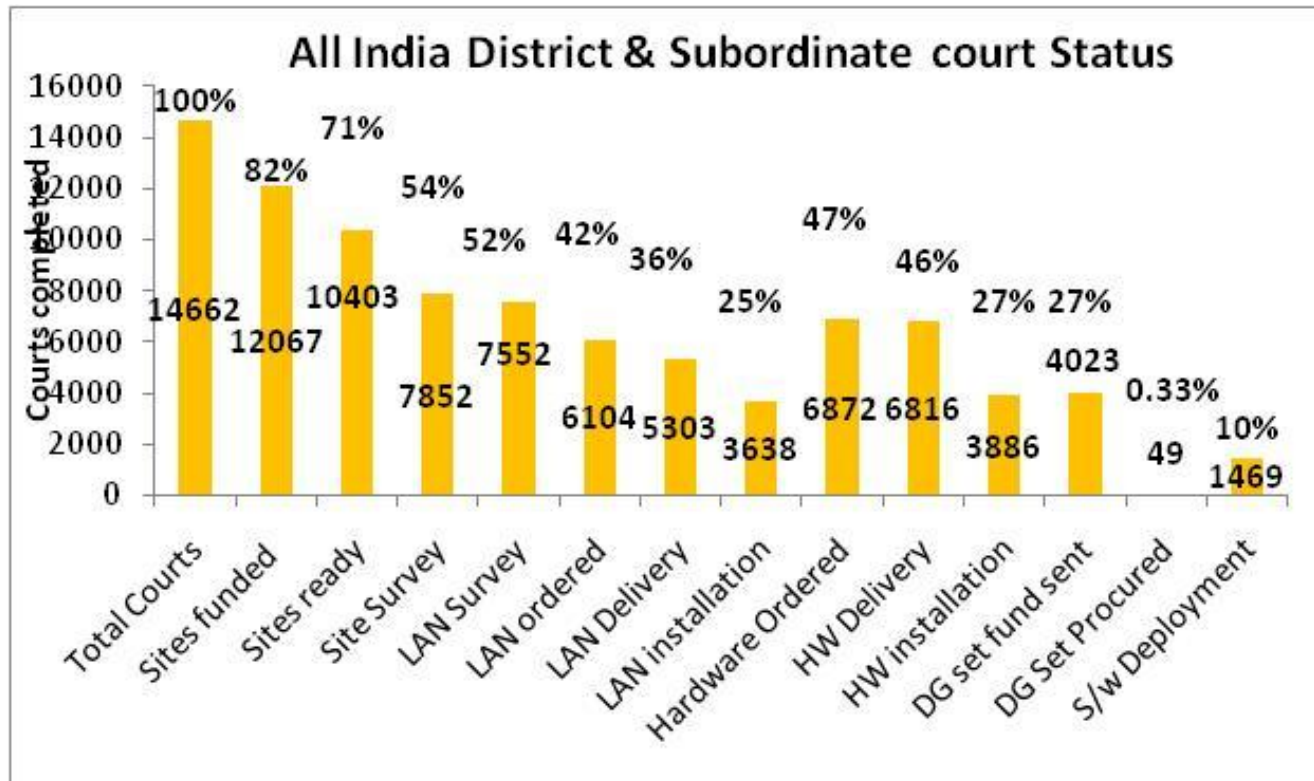

- ▶ **Supreme Court and High Courts -**
- ▶ Hardware upgraded at SC and 19 HCs, LAN upgraded at 8 HCs & 6 Benched, rest WIP
- ▶ **District and Subordinate Courts**
- ▶ Laptops -14309 Judicial Officers
- ▶ Internet connectivity - 9773 Judges, 1229 court complexes
- ▶ ICT Trainings - 9563 Judges, 36605 court staff
- ▶ **Financial Status –** Rs 398 Cr released, 348 Cr committed, Rs 203.5 Cr. disbursed

Progress in implementation in last fortnight

▶ Site Preparation

- ▶ **Gauhati HC** – 1 court complexes reported as ready in Tripura
- ▶ **Rajasthan HC** – 16 court complexes reported as ready.
- ▶ **Karnataka HC** – 2 court complexes reported as ready.

▶ LAN survey

- ▶ **Shimla HC** - LAN Survey completed at 2 district court complexes and PO initiated.
- ▶ **Karnataka HC** - LAN survey completed for Bagalkot district court complex.

▶ LAN Delivery and installation

- ▶ **Calcutta HC** – PO issued for LAN installation at 9 taluka court complexes
- ▶ **Orissa HC** – PO issued for LAN installation at 2 court complexes.
- ▶ **Bombay HC** - LAN installation completed at 6 court complexes in Bombay.

▶ Hardware Delivery and installation


- ▶ **Calcutta HC** – H/W installation completed at 1 district Court Complex, thus hardware installation completed at 22/22 District Court Complexes.
- ▶ **Bombay HC** – Hardware item delivery completed at 1 court complex, thus hardware delivery completed at all 133 District Court Complexes.

▶ Technical Manpower

- ▶ **Rajasthan High Court** – PO for extension of 3 SO issued. 2 SOs deployed.
- ▶ **Kerala High Court** – One SO deployed


Allahabad – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Hardware – (Vendor : M/s HCL)
 - ▶ Order given in March'09 for all 70 CCs (1928 courts)
 - ▶ Delivery completed in June 2009.
 - ▶ Installation completed at only 37 courts
 - ▶ Partial installation at remaining courts
 - ▶ Issues – SNR, power points/earthing missing
 - ▶ LAN –
 - ▶ Order given in Aug'09 and Jan'10 for all 42 DCCs and 19 taluka CCs (1255 courts)
 - ▶ Delivery completed at all district courts & 13 talukas.
 - ▶ Installation under progress at 35 DCs and 13 TCCs and not started at 7 DCCs and 6 taluka CCs .
 - ▶ Issues in installation – SNR, power points / earthing missing etc.
 - ▶ Resurvey LAN POs issued for 20 / 27 CCs.
- ▶ Technical Manpower – 63 / 70 System Officers (SOs). CVs required by HC for remaining posts.
- ▶ **Issues / Action Points:**
 - ▶ Sites found as not ready by vendor at most of 70 DCs
 - ▶ Site not ready at taluka courts.
 - ▶ Vendor to complete LAN survey at 28 / 70 DCs and HC to affirm site readiness for these sites.
 - ▶ DG Set – Cost estimates yet to be received from HC.

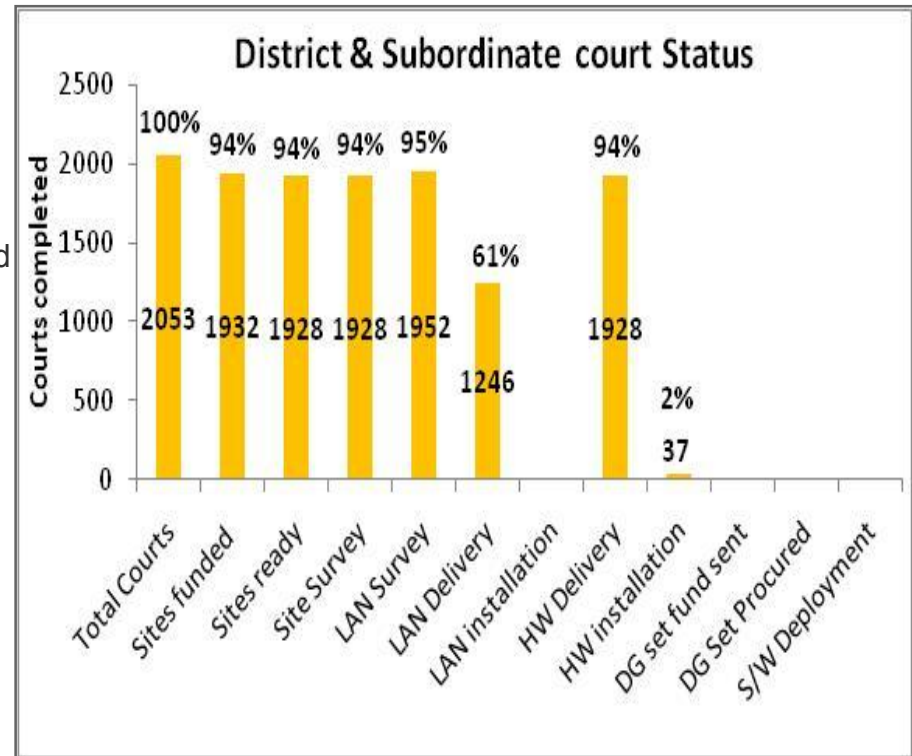

Andhra Pradesh – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Sites Ready–50/51 court complexes (497/505 courts)
 - ▶ Hardware order issued for 26 CC(302 courts)
 - ▶ LAN Order issued for 34 CC (401 courts).
 - ▶ **Application Software** – Feedback received. customization under progress for deployment at ready courts.
 - ▶ **Technical Manpower** - 17 / 23 System Officers (SOs), 17 / 36 Systems Assistants (SAs) deployed.
- ▶ **Issues:**
 - ▶ Site preparation funds to be sent for 246 / 297 court complexes (432 courts). Estimates received.
 - ▶ Hardware / LAN orders issued to Wipro cancelled for 16 CCs (96 courts). Resurvey order given to HCL
 - ▶ Technical manpower have not reported post joining
 - ▶ DG set procurement /installation to be taken up
 - ▶ Software deployment to be planned at sites where installation completed

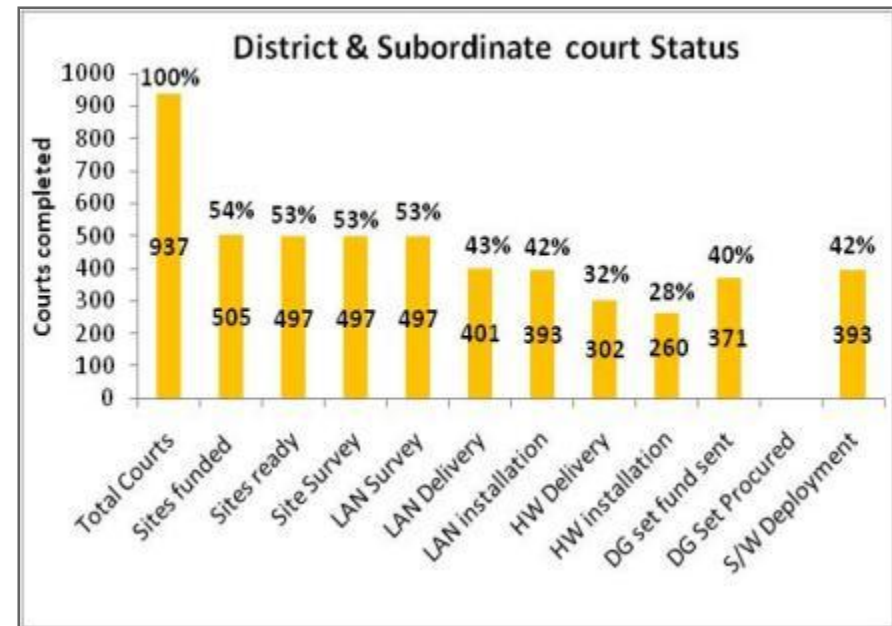

Bombay – Status and Progress


- ▶ LAN installation completed at 6 CCs, HW installation completed at 32 CCs

▶ Overall status:

- ▶ Sites Ready–136/468 CCs (497/505 courts)
- ▶ Hardware order issued for 133 / 136 CCs (1205 courts). LAN order issued for 79CCs (836 courts).
- ▶ **Application Software** – No customization required.
- ▶ **Technical Manpower** - 15 / 34 SOs, 7 / 66 SAs deployed.


▶ Issues / Action Points:

- ▶ Software deployment to be planned at ready sites
- ▶ 332 CCs yet to be funded for site preparation. Estimates received -217 CCs.
- ▶ Estimates to be sent by HC for balance CCs.
- ▶ Hardware and LAN installation to be completed at remaining sites by the vendor.
- ▶ Pending Technical manpower to be recruited.
- ▶ DG set procurement and installation to be taken up by the HC.

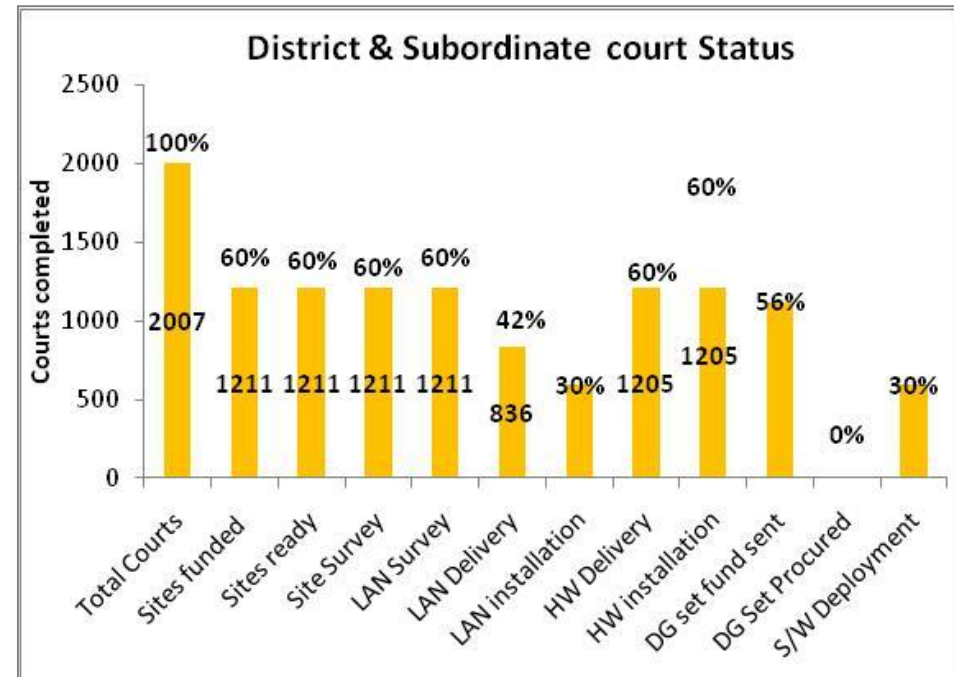


Calcutta – Status and Progress

- ▶ **H/W installation completed at 1 district Court Complex; LAN PO issued for 9 taluka CC**
- ▶ **Overall status**
 - ▶ Sites Ready – 771 / 777 courts
 - ▶ Hardware order issued for 619 courts and LAN for 372 courts
 - ▶ Software deployed at courts where Hardware / LAN installed
 - ▶ Technical manpower - 20/20 SOs, 16 / 40 SAs
- ▶ **Issues / Action Points:**
 - ▶ Hardware installation to be completed at taluka sites by the vendor.
 - ▶ LAN survey reports to be finalized at NIC HQ by the vendor for remaining courts.
 - ▶ Hardware / LAN orders to be issued for these ready courts.
 - ▶ Hardware and LAN not completed at Andaman bench as site is not ready. Site to be readied by the Bench authorities.
 - ▶ DG Set procurement to be expedited by the High Court at district courts. Estimates to be sent by the HC to NIC for taluka courts.

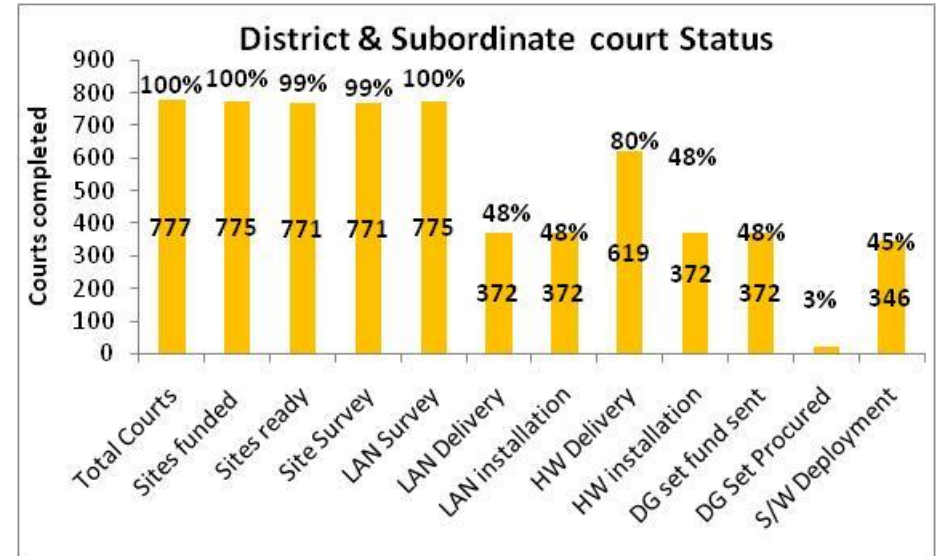


Chhattisgarh – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status**
 - ▶ Sites Ready – 16 CC (198 courts)
 - ▶ Hardware and LAN order issued for 14 CC (190 courts).
 - ▶ Software deployed at 13 CC (183 courts) where Hardware / LAN installed
 - ▶ Technical manpower - 15 / 15 SOs, 6 / 24 SAs deployed
- ▶ **Issues / Action Points:**
 - ▶ Funds to be transferred for site preparation at 23 taluka court complexes.
 - ▶ Cost estimates to be sent by HC for site preparation at remaining 44 taluka court complexes.
 - ▶ HC to send DG set cost estimates as per guidelines to NIC HQ.
 - ▶ Pending hardware installation at 1 site to be completed by the vendor.

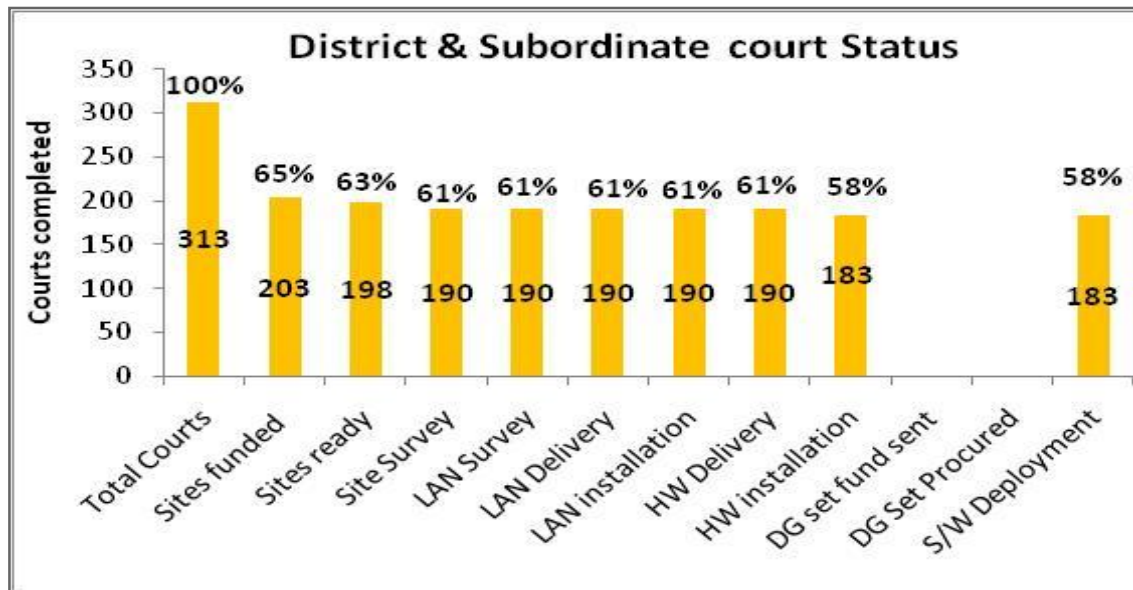


Gauhati – Status and Progress

- ▶ **1 court complexes reported as ready in Tripura**
- ▶ **Overall Status:**
 - ▶ Sites ready – 62 CC (298 courts)
 - ▶ Hardware order issued for 15 CC (78 courts) & LAN order for 13 CC (65 courts), building being shifted for balance 2 CCs in Nagaon district for which hardware issued.
 - ▶ Software deployed at pilot locations – Kamrup, Aizawl and Agaratala.
 - ▶ Technical manpower – 26 / 26 SOs and 0 / 14 SAs deployed
- ▶ **Issues / Action Points:**
 - ▶ Funds to be sent for sites preparation at 14 court complexes under Manipur state.
 - ▶ LAN POs to be issued for sites where survey completed by vendor (24 court complexes)
 - ▶ Pending site preparation to be completed at sites already funded.
 - ▶ DG Set procurement yet to be taken up by the High Court.
 - ▶ Vendor to complete pending site / LAN surveys at ready courts.

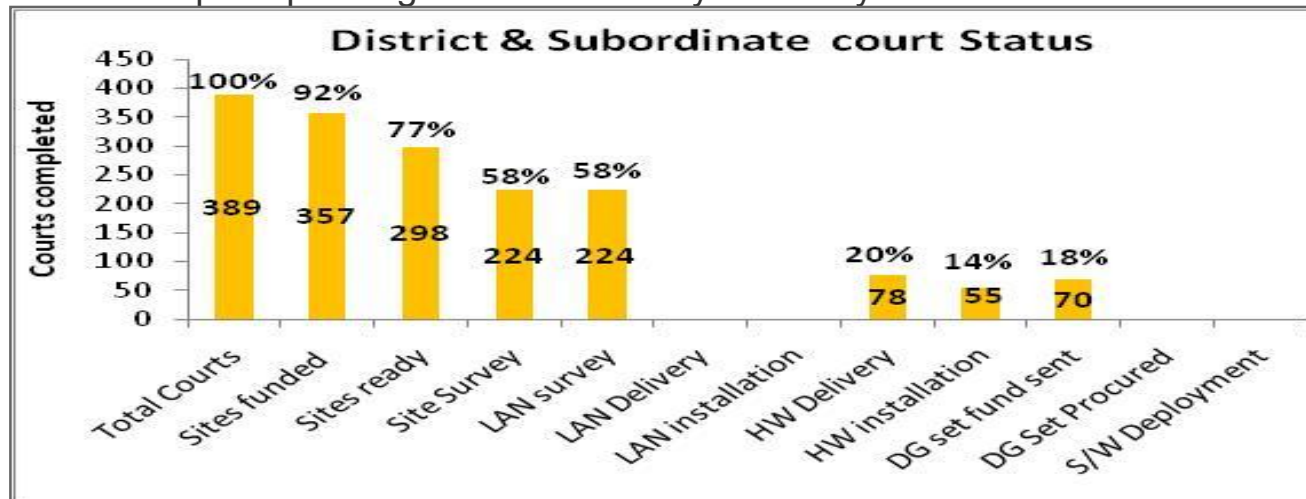


Gujarat – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Sites ready – 704 courts
 - ▶ Hardware and LAN order issued for 341 courts
 - ▶ Software deployed at 260 courts and under progress at remaining courts.
 - ▶ Technical manpower – 27 / 27 SOs and 0 / 38 SAs deployed
- ▶ **Issues / Action Points:**
 - ▶ Site Readiness proformas to be sent by the HC for 152 sites (363 courts) reported as ready.
 - ▶ Site preparation to be completed at the balance 40 court complexes not ready as on date.
 - ▶ DG Set procurement and installation to be taken up for 54 court complexes by the HC.
 - ▶ Technical manpower vendor to provide CVs for SA posts

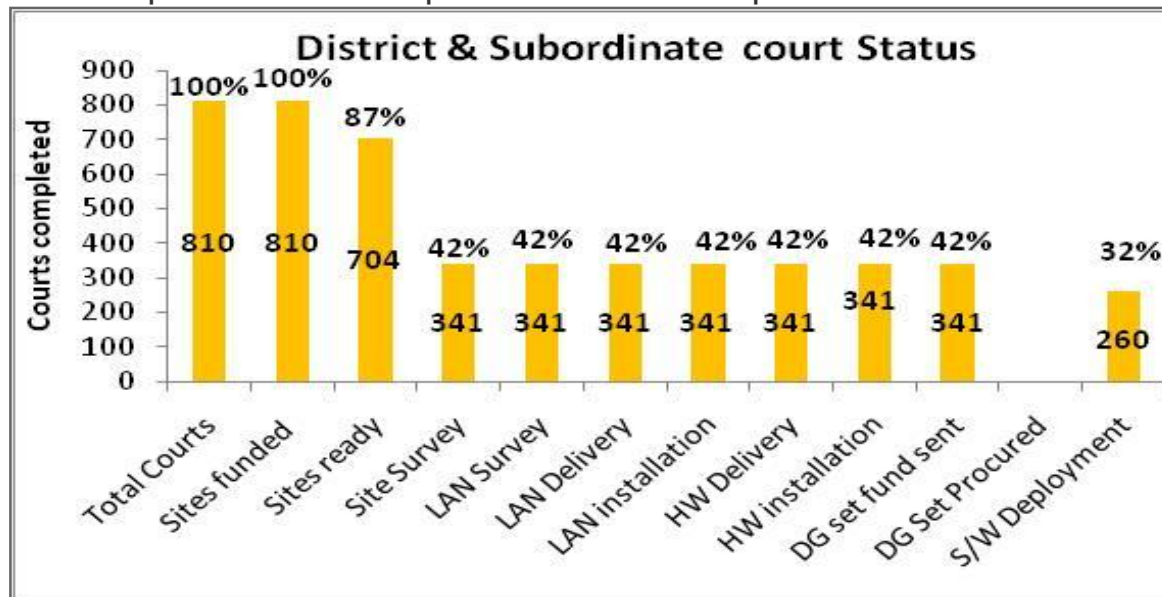


Jabalpur – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Hardware and LAN order issued for 640 courts
 - ▶ Software deployed at pilot site.
 - ▶ Technical manpower – 49 / 49 SOs and 0 / 86 SAs deployed. List awaited from HC for SAs
- ▶ **Issues / Action Points:**
 - ▶ Site preparation to be completed at 43 taluka court complexes where funds had been sent.
 - ▶ Site preparation cost estimates for balance 18 taluka court complexes to be sent by the HC
 - ▶ Funds to be sent for site preparation at 11 CCs for which estimates sent by the HC
 - ▶ Site Readiness proformas to be sent by the HC for 76 CCs reported as ready.
 - ▶ DG Set procurement and installation to be taken up by the HC
 - ▶ Vendor to complete pending hardware and LAN installation
 - ▶ HC to revise the DG set cost estimates for 5 sites as per circulated guidelines.
 - ▶ Software Roll out to be planned for courts where hardware / LAN installed.

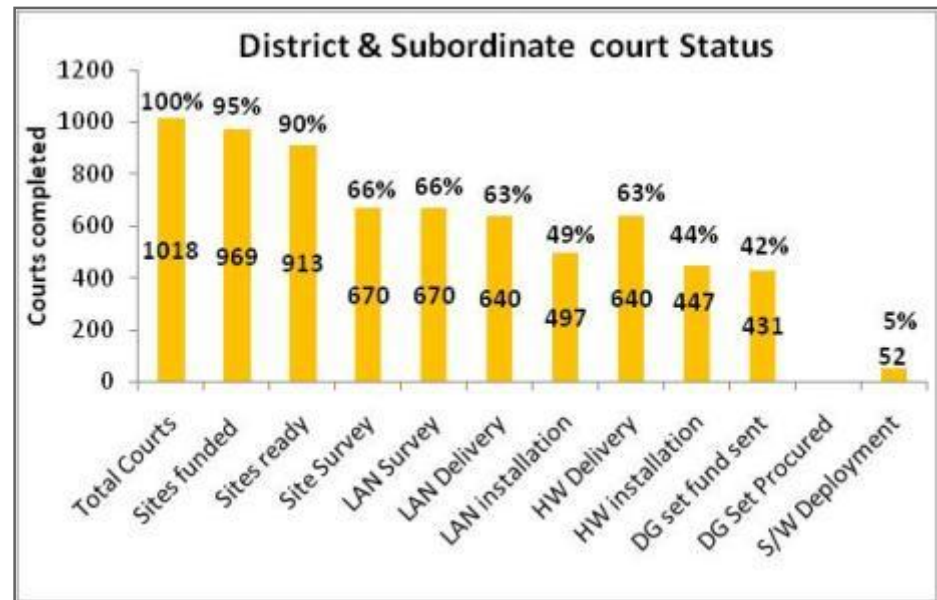


J&K – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at all 182 courts. Hardware and LAN order issued for 117 courts
 - ▶ Technical manpower – 22 / 22 SOs and 43 / 44 SAs deployed.
- ▶ **Issues / Action Points:**
 - ▶ Hardware installation to be completed at remaining sites by the vendor (M/s Wipro).
 - ▶ Software deployment to be planned at ready courts
 - ▶ DG Set procurement to be taken up by the High Court.
 - ▶ Orders for HW & LAN installation at Leh & Kargil district court complexes to be issued by NIC
 - ▶ M/s HCL to complete the site / LAN survey at Taluka court complexes

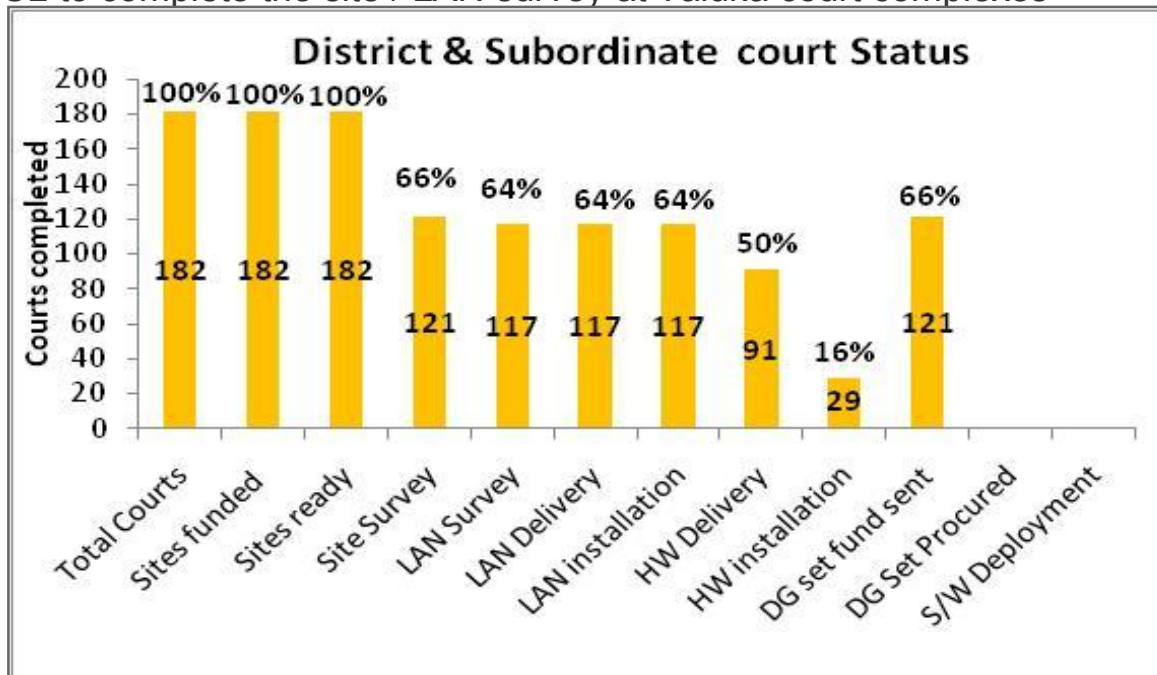


Jharkhand – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at 347 courts. Hardware order issued for 82 courts and LAN for 181 courts.
 - ▶ Technical manpower – 14 / 14 SOs deployed.
- ▶ **Issues / Action Points**
 - ▶ Site Preparation to be completed at pending sites.
 - ▶ Vendor to complete pending LAN surveys at 33 CC for which orders issued.
 - ▶ Vendor to complete hardware installation at 9 CC (82 courts).
 - ▶ Vendor to complete LAN delivery and installation for 27 CC (181 courts), orders recently issued.
 - ▶ NIC to issue hardware orders for 18 CC (99 courts).
 - ▶ Application software to be rolled out at pilot site.

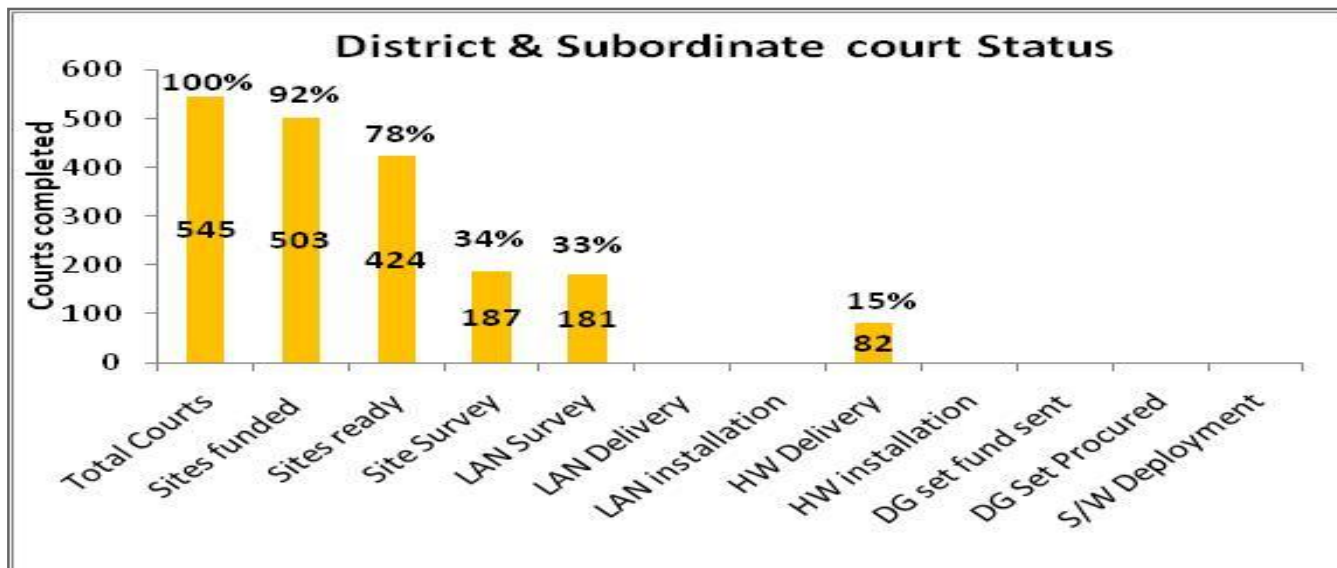


Karnataka – Status and Progress in last 2 weeks

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at 623 courts. Hardware and LAN order issued for 62 courts
 - ▶ Technical manpower – 7 / 29 SOs and 2 / 10 SAs deployed. New batch to be deployed from 23 Aug.
- ▶ **Issues / Action Points:**
 - ▶ Pending site preparation to be completed
 - ▶ Site preparation funds to be sent for 25 court complexes to the HC.
 - ▶ Vendor to complete site / LAN surveys at the ready sites.
 - ▶ Vendor to complete hardware installation, and LAN delivery / installation at 62 courts.
 - ▶ Funds for DG sets to be sent by NIC to the HC

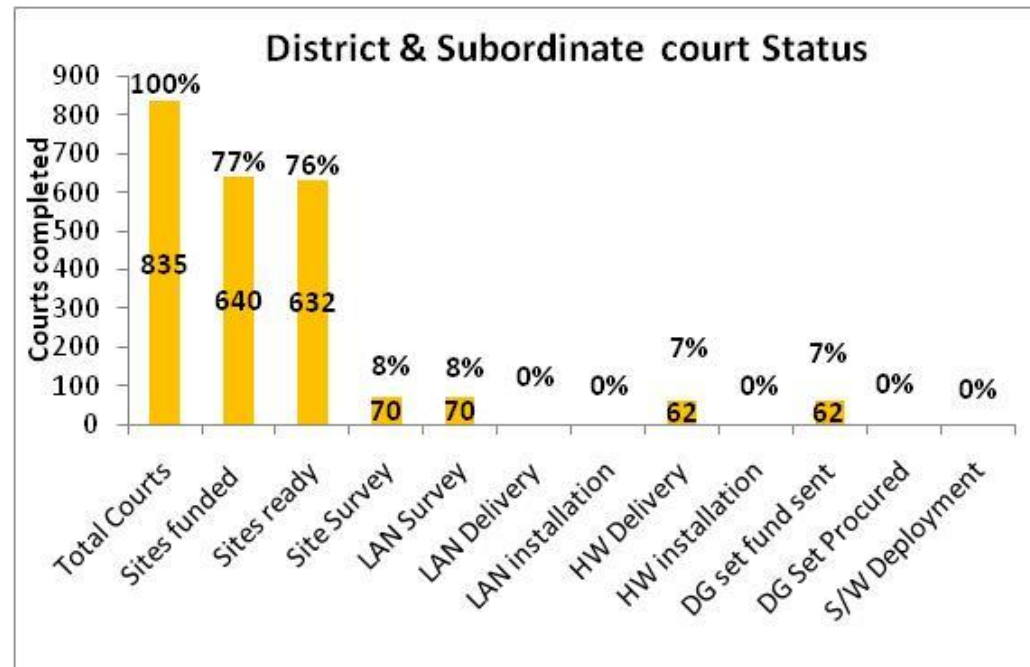


Kerala – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at all 404 courts. Hardware and LAN order issued for 229 courts
 - ▶ Software deployed at 223 courts.
 - ▶ Technical manpower – 10 / 14 SOs and 16 / 28 SAs deployed.
- ▶ **Issues / Action Points:**
 - ▶ **Site survey proformas awaited for 75 ready Taluka court complexes.**
 - ▶ Selection for pending technical manpower to be completed by the HC.
 - ▶ DG Set procurement to be taken up by the High Court.

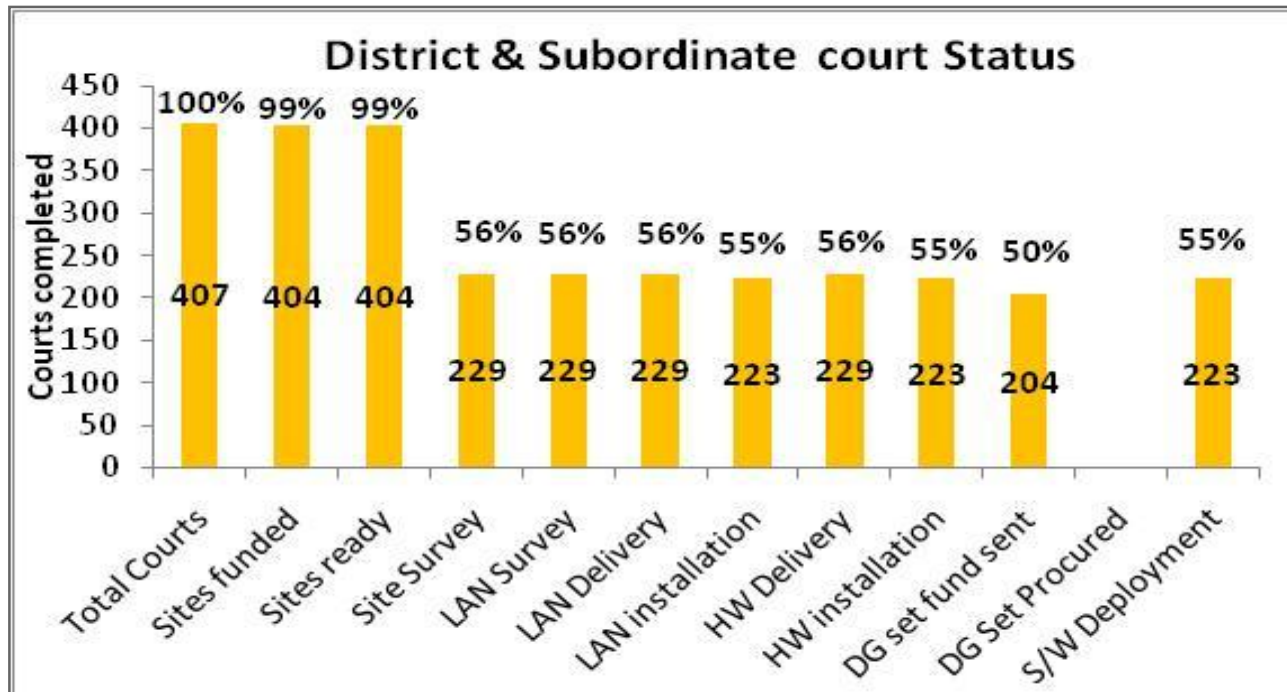


Madras – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at all 527 courts.
 - ▶ Hardware and LAN order issued and installation completed at 325 courts
 - ▶ Software deployed at 325 courts.
 - ▶ Technical manpower – 29 / 31 SOs and 43 / 60 SAs deployed.
- ▶ **Issues / Action Points:**
 - ▶ Pending site preparation to be completed
 - ▶ Plan for data entry to be formulated for courts where software deployed.
 - ▶ DG Set procurement to be taken up by the HC.
 - ▶ Manpower selection to be completed by the HC for locations where CVs available. Pending CVs to be provided by the vendor

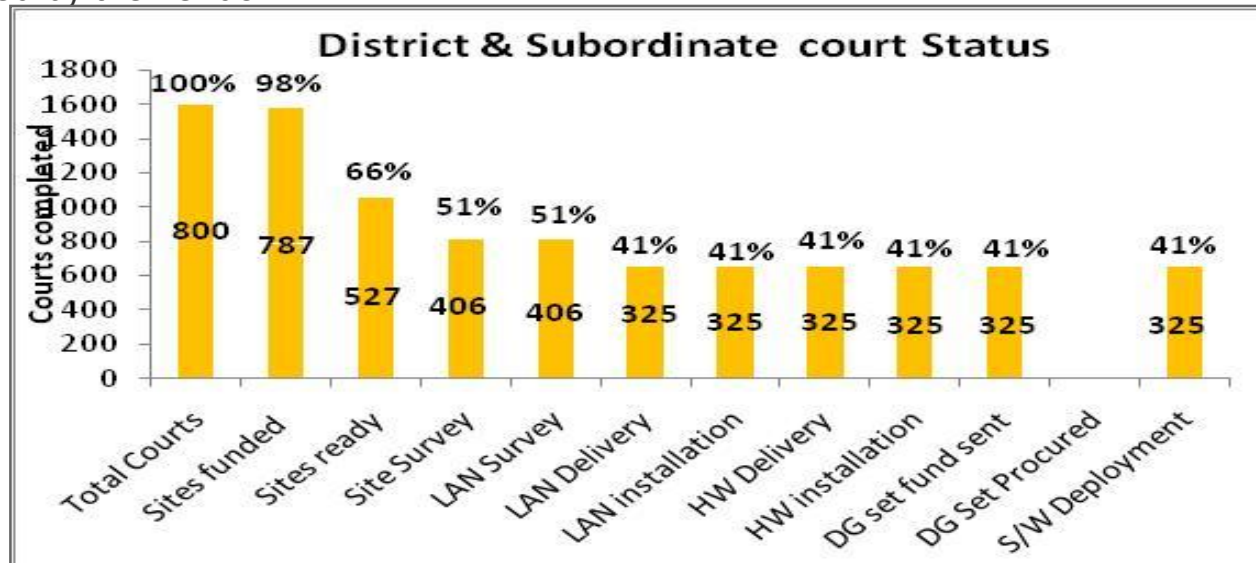


Sikkim – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Issues / Action Points:**
 - ▶ Pending site preparation fund to be sent by NIC HQ to HC.
 - ▶ Vendor to complete LAN installation at the HC.
 - ▶ Pilot site for application software to be identified by the HC.

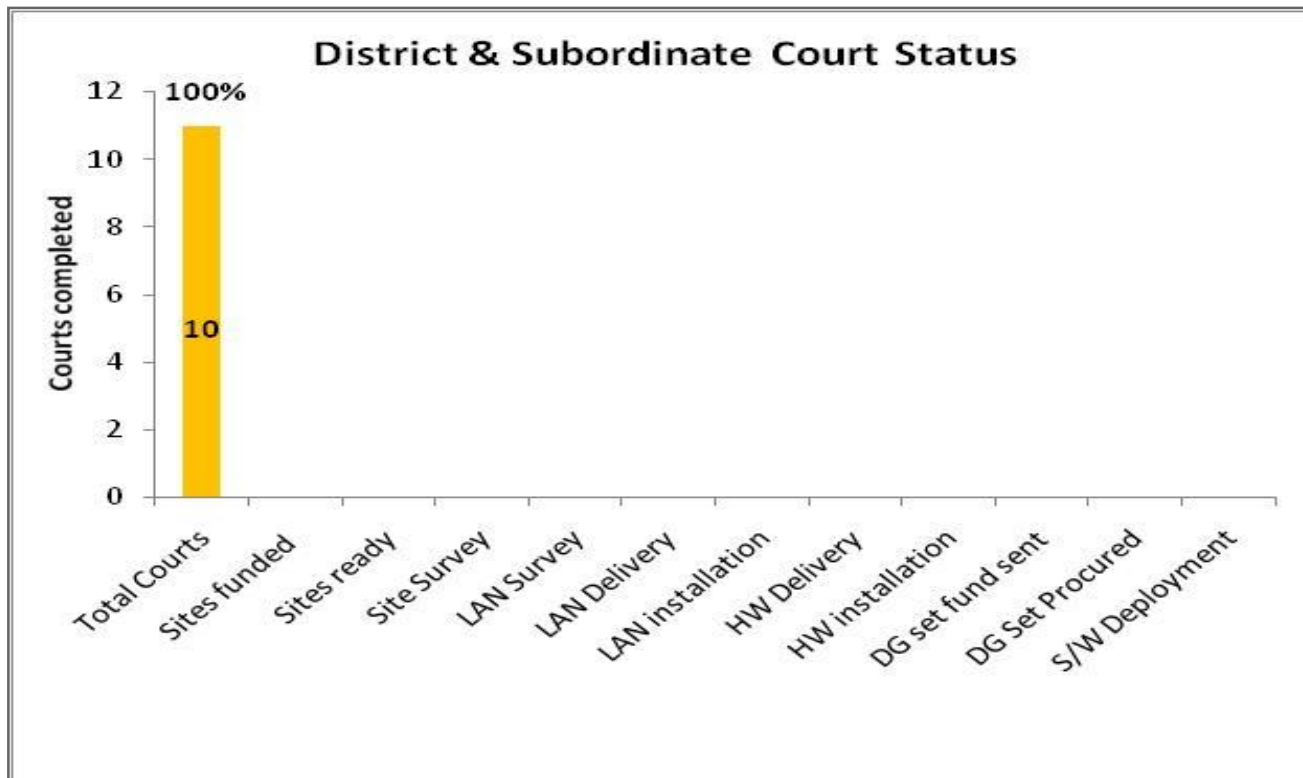


Shimla – Status and Progress

- ▶ **LAN Survey completed at 2 district court complexes and PO initiated.**
- ▶ **Overall status:**
 - ▶ Site ready at all 103 courts. Hardware order issued for 29 courts
 - ▶ Technical manpower – 11/ 11 SOs deployed.
- ▶ **Issues / Action Points:**
 - ▶ Vendor to take up installation at District Court Shimla.
 - ▶ **HC to provide sign off on LAN survey reports submitted by the vendor. Pending with the HC for last 2-3 weeks. Delay in issuance of LAN / hardware purchase orders.**
 - ▶ Software cannot be deployed at any pilot site as LAN not available at any site.
 - ▶ HC to revise the DG Set cost estimates in accordance with the circulated DG Set guidelines.

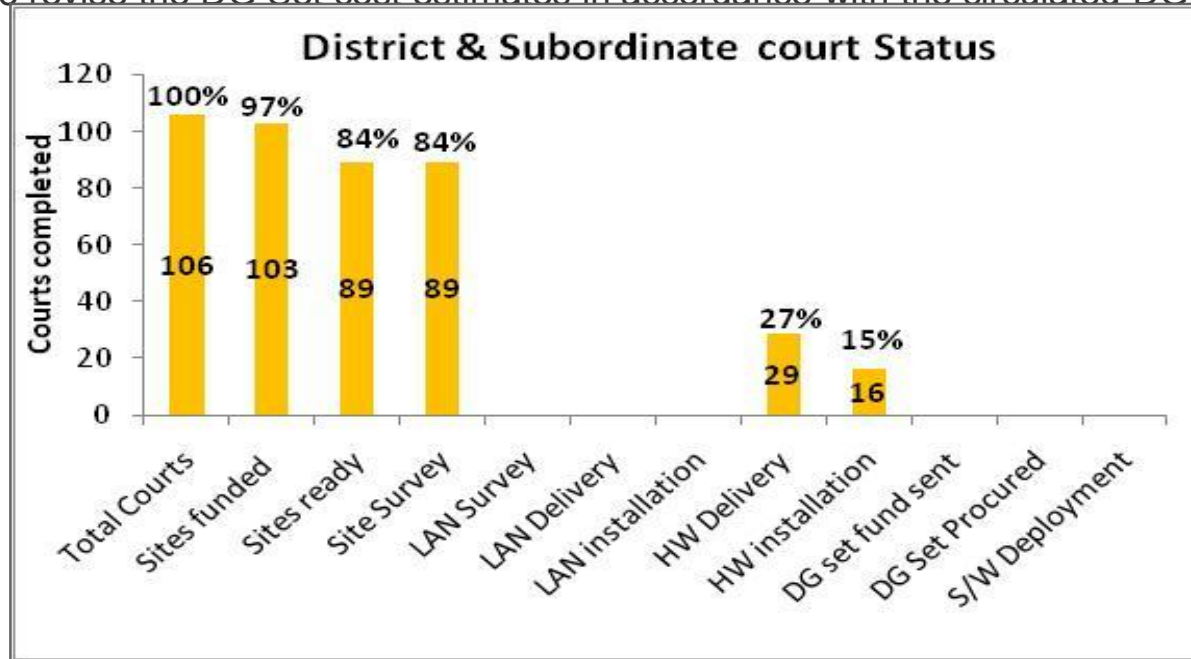


Punjab Haryana – Status and Progress

- ▶ **No progress in the last fortnight**
- ▶ **Overall status:**
 - ▶ Site ready at all 672 courts. Hardware & LAN order issued for 459 & 510 courts
 - ▶ Technical manpower – 33 / 33 SOs , 27 / 66 SAs deployed.
- ▶ **Issues / Action Points:**
 - ▶ Hardware and LAN installation to be completed at remaining sites by the vendor.
 - ▶ Pending system assistant's selection to be completed by the HC.
 - ▶ DG Set procurement to be taken up by the High Court.

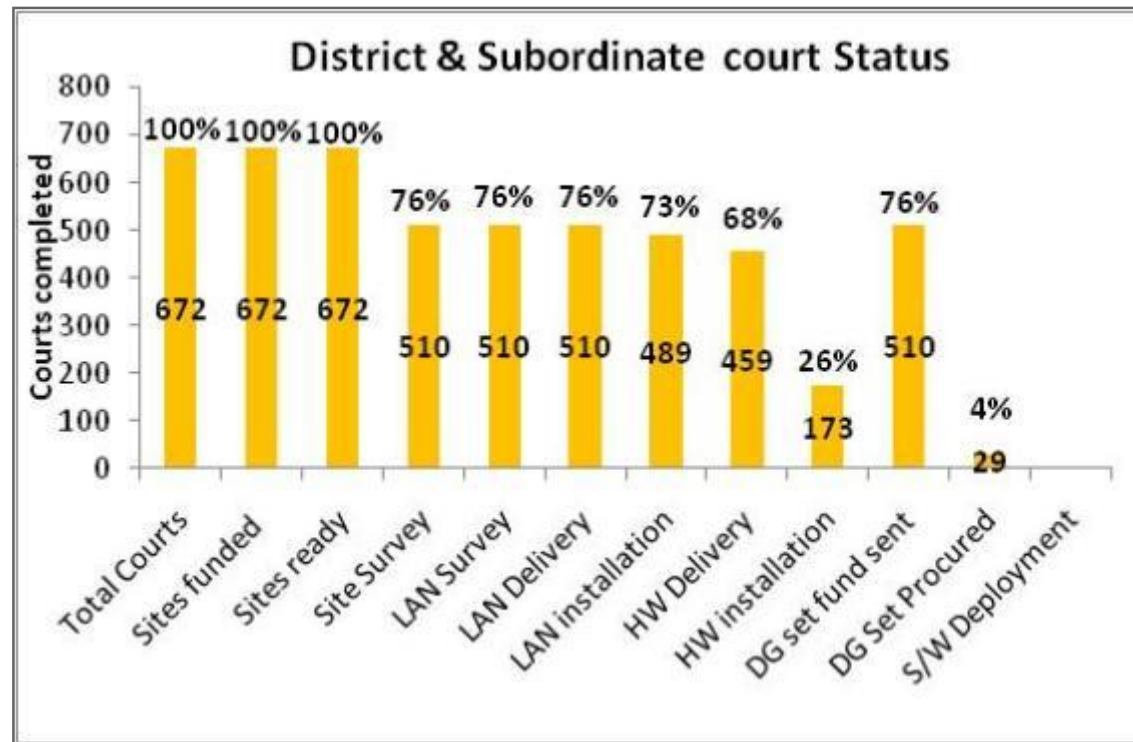

Orissa – Status and Progress


- ▶ **Overall status:**
 - ▶ Site ready at 141 courts. Hardware order issued for 32 courts and LAN order under process
 - ▶ Application software deployed at the pilot site
 - ▶ Technical manpower – 14 / 14 System Officers (SOs) deployed.
- ▶ **Issues / Action Points:**
 - ▶ HC is to revert to NIC on the requirement of site preparation funds, if any.
 - ▶ HC to complete pending site preparation
 - ▶ Only 5 / 36 sites found as ready (3 District and 2 taluka) by the vendor on site survey.
 - ▶ HC to close the gaps found in site readiness in the remaining 31 sites by sending the site readiness proformas for these 26/31 sites after getting them filled up by the court nodal officers.

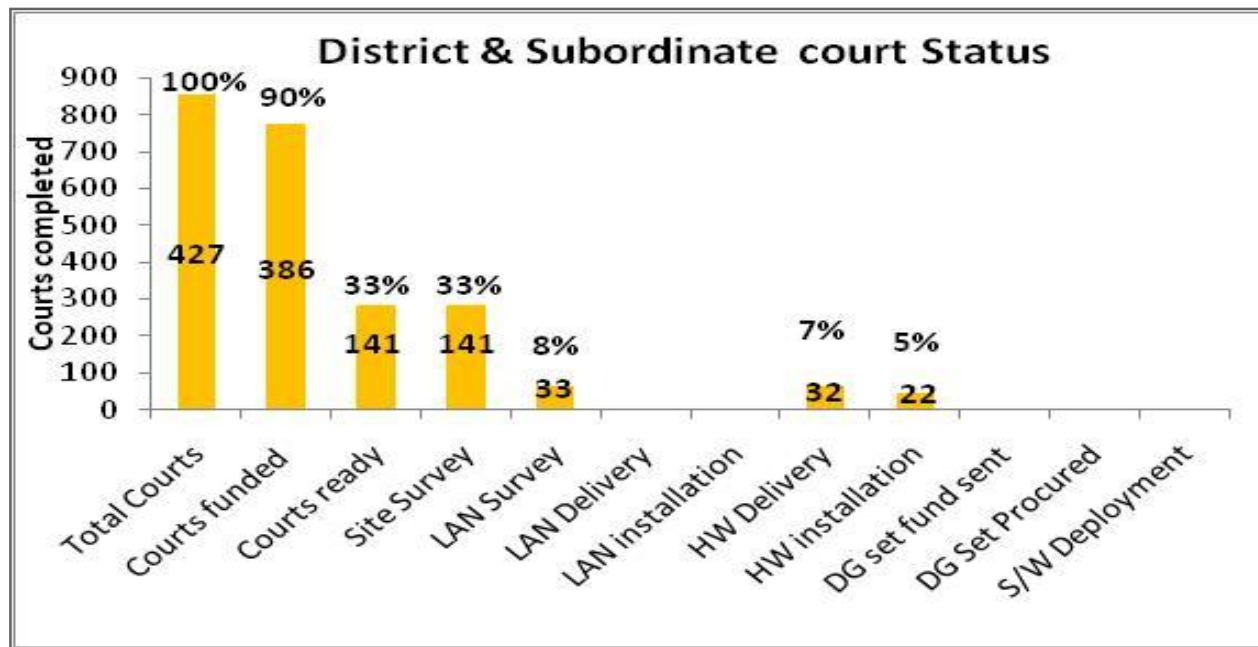

Patna – Status and Progress


- ▶ **Site / LAN Survey order issued for 2 ready sites**
- ▶ **Issues / Action Points:**
 - ▶ Funds sent for 117 sites, 2 sites reported as ready till date.
 - ▶ Site / LAN Survey under progress at these 2 sites
 - ▶ No computerization can hence be taken up for these sites. HC to complete pending site preparation on priority basis.
 - ▶ HC to send the site preparation cost estimates for balance court complexes to NIC HQ

** - no. of courts covered through site preparation funds to be confirmed in entirety.*

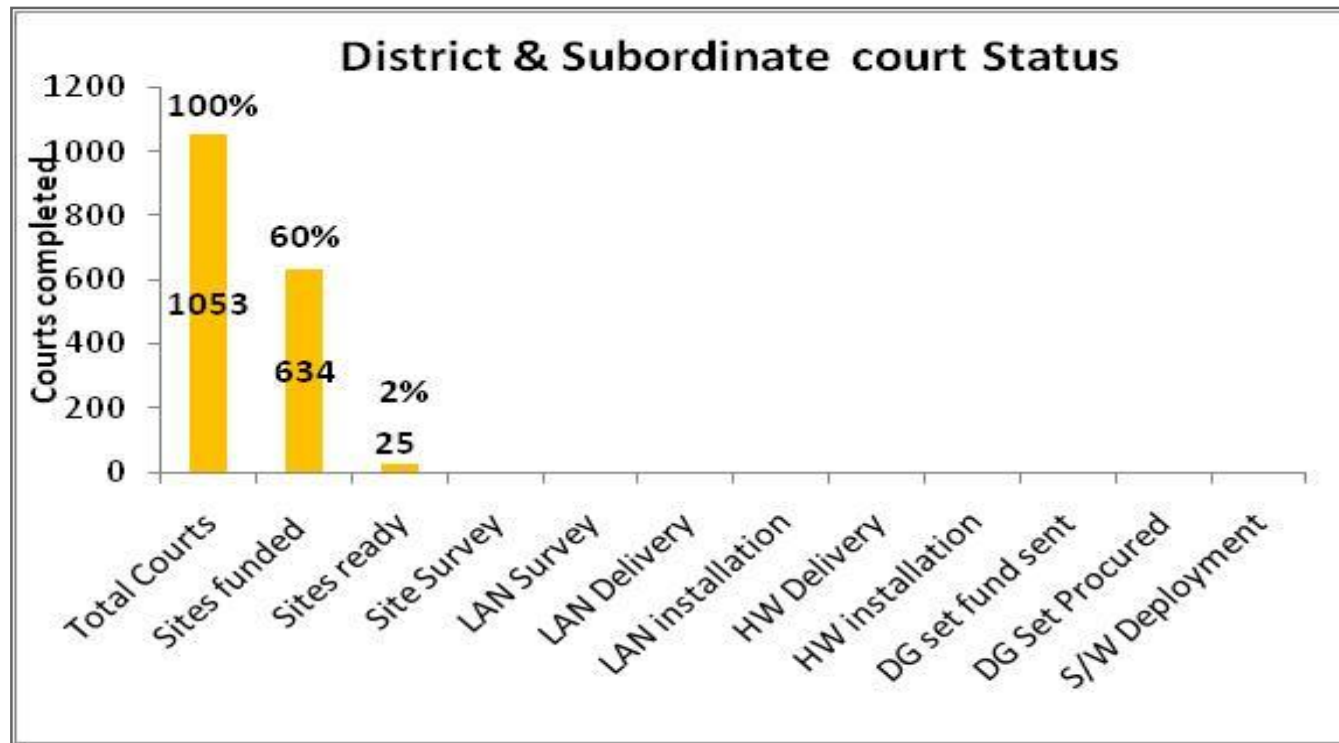


Rajasthan – Status and Progress

- ▶ Sites reported as ready at 16 court complexes.
- ▶ Overall status:
 - ▶ Site ready at 129 CC (562 courts).
 - ▶ Hardware order issued for 108 courts . LAN order issued for 94 courts.
 - ▶ Technical manpower – 28 / 31 SOs , 2 / 2 SAs deployed.
- ▶ Issues / Action Points:
 - ▶ HC to complete pending site preparation work at remaining courts
 - ▶ HC to select and deploy pending technical manpower
 - ▶ Vendor to complete site / LAN survey in balance ready sites
 - ▶ **NIC to send DG set funds for sites where hardware / LAN orders issued**
 - ▶ Vendor to complete pending hardware & LAN installation

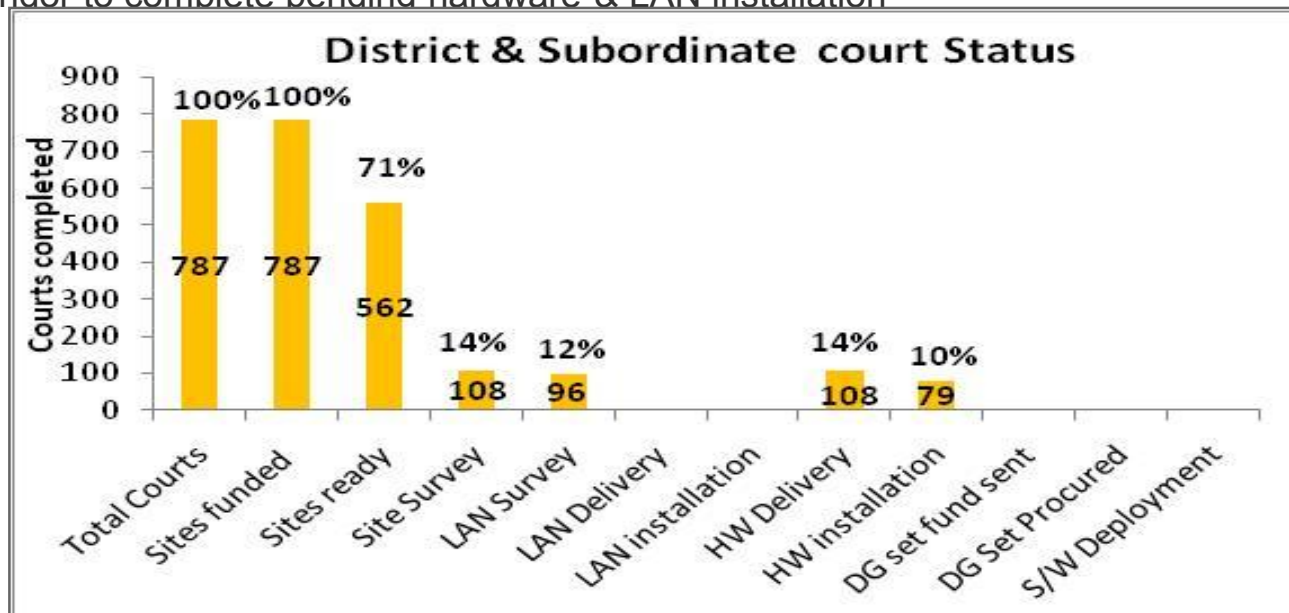

Uttarakhand – Status and Progress

- ▶ *No progress in the last fortnight*
- ▶ **Issues / Action Points:**
 - ▶ Pending site preparation to be completed
 - ▶ Hardware delivery and installation to be completed at remaining sites by the vendor.
 - ▶ LAN PO to be issued for sites where Hardware PO is issued.
 - ▶ DG Set procurement to be done

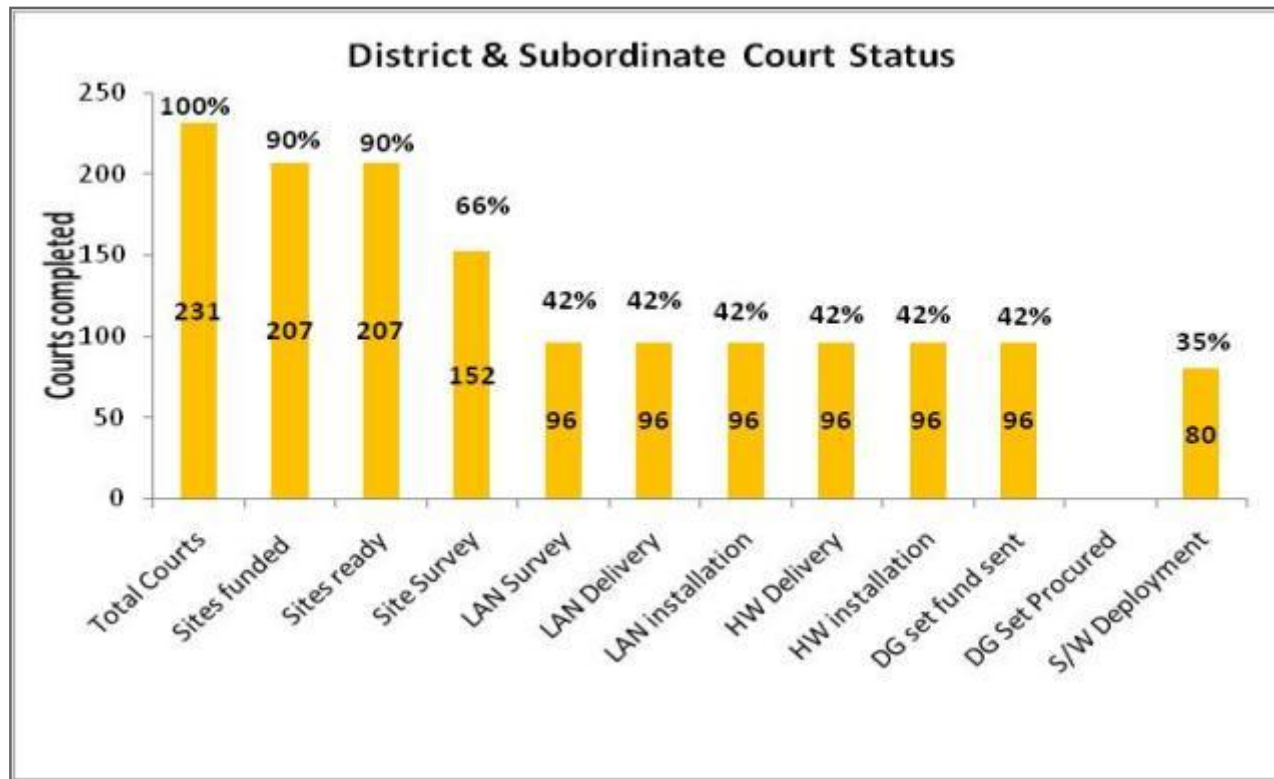

THANK YOU.
